



Appendix B

Compaction Curves

Report No: MDD:CAN20S-17343
Issue No: 1

Maximum Dry Density Report

Client: Toni O'Regan
City Care Limited
PO Box 7669
Sydenham

Christchurch 8240
NZ

Project: QA Testing - City Care Ltd


The tests reported herein (unless otherwise indicated) have been performed in accordance with the laboratory's scope of accreditation. Samples are tested as received, in natural condition, unless stated otherwise in the comments. This report may only be reproduced in full.



The results in this report relate only to the items / samples that were tested

Approved Signatory: Rebecca Royfee
(Laboratory Technician)
IANZ Accreditation No:200
Date of Issue: 23/10/2020

Sample Details

Sample ID: CAN20S-17343

Material: Sand

Site/Sampled From: CD2 Prestons - Stage 5 East side of S/P

Specification: Vibrating Hammer Compaction Test

Sampling Method: Stated to be NZS 4407:2015 2.4.6.5

Technician: Laura Cranston

Client Sample ID: 1691/20

Sample Source: Miscellaneous Material Source


Date Sampled: 20/10/2020

Sampled By: Advised - See Comments

Date Tested: 22/10/2020

Sampling Endorsed?: No

Dry Density - Moisture Relationship

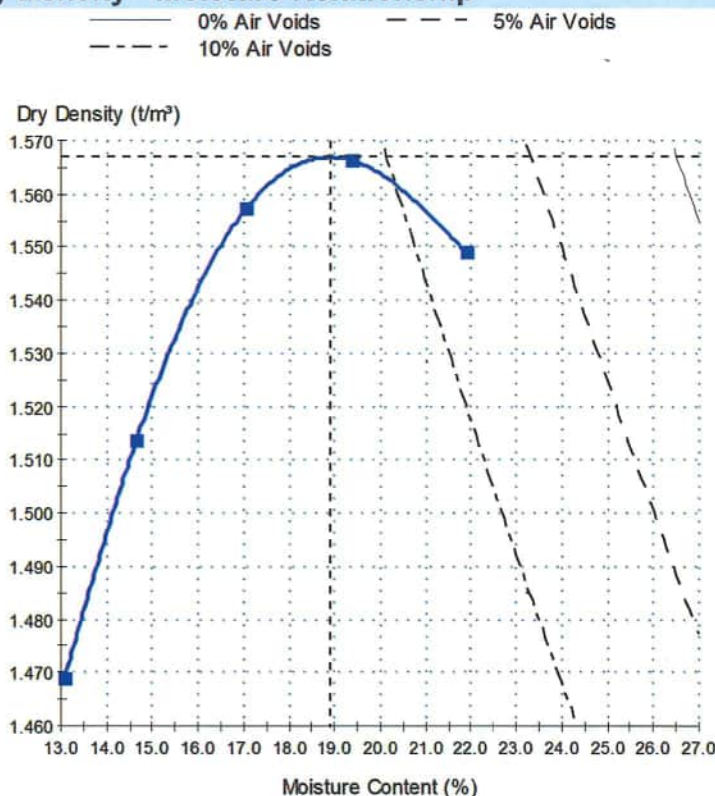

Test Results

NZS 4402:1986 Test 4.1.3 - 1986

Maximum Dry Density (t/m³): 1.56

Optimum Moisture (%): 19

Solid Density (t/m³): 2.68 assumed

Fraction Tested Passes (mm): 37.5

Material Removed (%): 0

Sample History: Natural

Tested By: Laura Cranston

Date Tested: 22/10/2020

Comments

Sampled by A Hadlee

Maximum Dry Density Report

Report No: MDD:CAN20S-01176
Issue No: 1

Client: Toni O'Regan
City Care Limited
PO Box 7669
Sydenham

Christchurch 8240
NZ

Project: QA Testing - City Care Ltd

The tests reported herein (unless otherwise indicated) have been performed in accordance with the laboratory's scope of accreditation. Samples are tested as received, in natural condition, unless stated otherwise in the comments. This report may only be reproduced in full.

IANZ
ACCREDITED LABORATORY



Approved Signatory: Max Burford
(Supervisor)
IANZ Accreditation No:200
Date of Issue: 22/01/2020


Sample Details

Sample ID: CAN20S-01176
Material: Sand
Site/Sampled From: CDL Prestons Road
Specification: Vibrating Hammer Compaction Test
Sampling Method: Not Advised
Technician: Atu Rova

Client Sample ID: 0055/20 Sample 3
Sample Source: Miscellaneous Material Source
Date Sampled: 20/01/2020
Sampled By: Advised - See Comments
Date Tested: 21/01/2020
Sampling Endorsed?: No

Dry Density - Moisture Relationship

———— 0% Air Voids - - - 5% Air Voids
- - - - 10% Air Voids

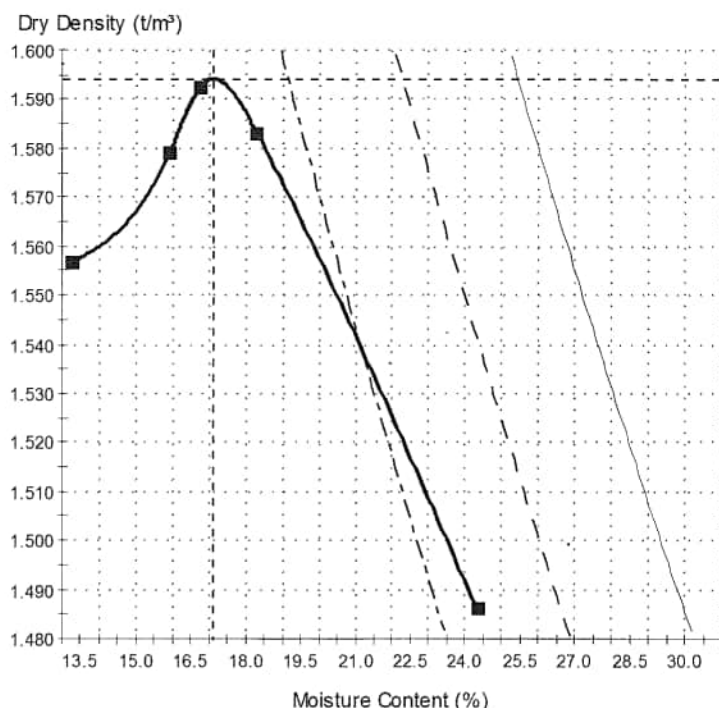

Test Results

NZS 4402:1986 Test 4.1.3

Maximum Dry Density (t/m³): 1.60
Optimum Moisture (%): 17
Solid Density (t/m³): 2.68 assumed
Fraction Tested Passes (mm): 37.5
Material Removed (%): 0
Sample History: Natural
Tested By: Atu Rova
Date Tested: 21/01/2020

Comments

* Sample 3
* Material sampled by Clive Gould.

Maximum Dry Density Report

Report No: MDD:CAN20S-01175
Issue No: 1

Client: Toni O'Regan
City Care Limited
PO Box 7669
Sydenham

Christchurch 8240
NZ

Project: QA Testing - City Care Ltd

The tests reported herein (unless otherwise indicated) have been performed in accordance with the laboratory's scope of accreditation. Samples are tested as received, in natural condition, unless stated otherwise in the comments. This report may only be reproduced in full.




Approved Signatory: Max Burford
(Supervisor)
IANZ Accreditation No:200
Date of Issue: 22/01/2020

Sample Details

Sample ID: CAN20S-01175
Material: Sand
Site/Sampled From: CDL Prestons Road
Specification: Vibrating Hammer Compaction Test
Sampling Method: Not Advised
Technician: Atu Rova

Client Sample ID: 0054/20 Sample 2
Sample Source: Miscellaneous Material Source
Date Sampled: 20/01/2020
Sampled By: Advised - See Comments
Date Tested: 21/01/2020
Sampling Endorsed?: No

Dry Density - Moisture Relationship

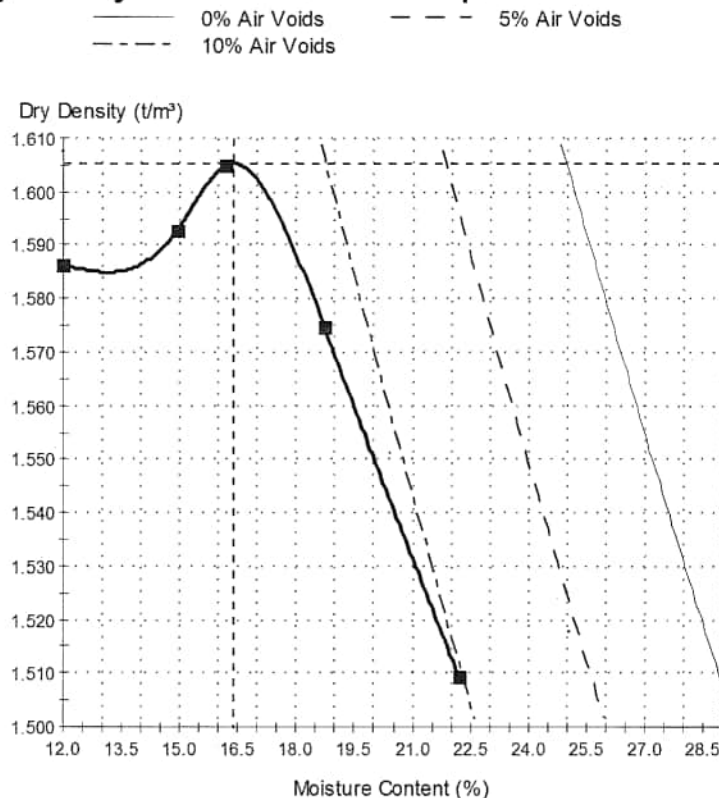

Test Results

NZS 4402:1986 Test 4.1.3

Maximum Dry Density (t/m³): 1.60
Optimum Moisture (%): 16
Solid Density (t/m³): 2.68 assumed
Fraction Tested Passes (mm): 37.5
Material Removed (%): 0
Sample History: Natural
Tested By: Atu Rova
Date Tested: 21/01/2020

Comments

* Sample 2
* Material sampled by Clive Gould.

Maximum Dry Density Report

Client:

City Care Limited
PO Box 7669
Sydenham

Christchurch 8240
NZ

Project:

City Care



The tests reported herein (unless otherwise indicated) have been performed in accordance with the laboratory's scope of accreditation. Samples are tested as received, in natural condition, unless stated otherwise in the comments. This report may only be reproduced in full.



The results in this report relate only to the items / samples that were tested


Approved Signatory: Liam Brennan
(Laboratory Technician)
IANZ Accreditation No:200
Date of Issue: 29/01/2021

Sample Details

Sample ID: CAN21S-00814
Material: Silty Sand
Site/Sampled From: Ex Oakbridge, Eastern BDY Reserve
Specification: Vibrating Hammer Compaction Test
Sampling Method: As Received - Not Accredited
Technician: Maciej Gaworecki

Client Sample ID: Lab Ref: 0095/21
Sample Source: Miscellaneous Material Source
Date Sampled: 27/01/2021
Sampled By: Advised - See Comments
Date Tested: 28/01/2021
Sampling Endorsed?: No

Dry Density - Moisture Relationship

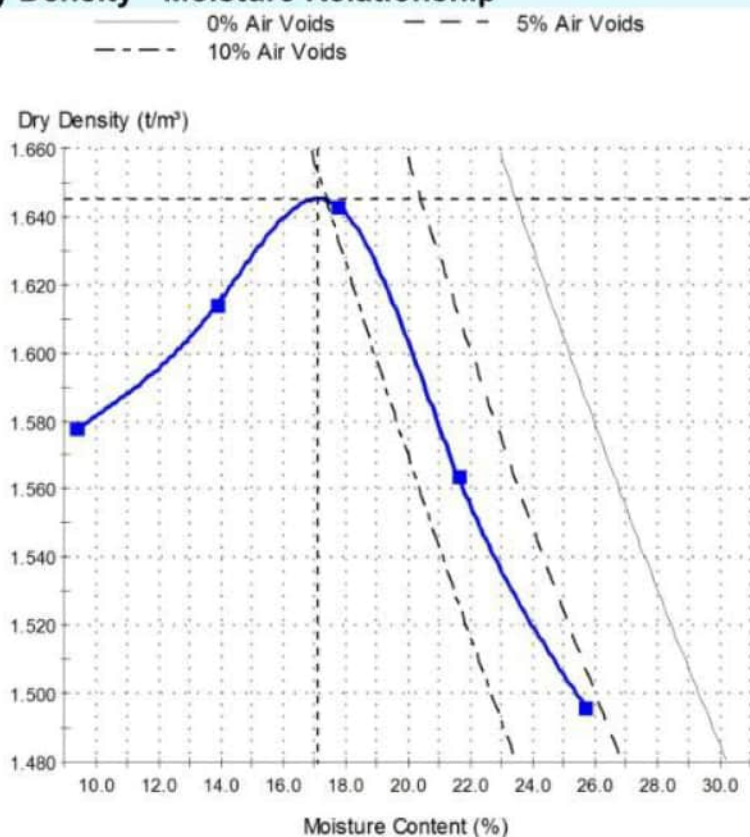

Test Results

NZS 4402:1986 Test 4.1.3 - 1986

Maximum Dry Density (t/m³): 1.64
Optimum Moisture (%): 17
Solid Density (t/m³): 2.68 assumed
Fraction Tested Passes (mm): 37.5
Material Removed (%): 0
Sample History: Natural
Tested By: Maciej Gaworecki
Date Tested: 28/01/2021

Comments

Compaction for test points @ 21.6% & 25.7% ceased prior to 3 minutes due to oversaturation causing ejection of fines from sample.
Material sampled by Clive Gould

Test Report


Client:	K.B. Contracting & Quarries Limited	Sample Date:	08/12/2017	08:00
Address:	PO Box 19746, Woolston, Christchurch 8241	Sampled By:	Pete Haward	
Client Ref:	Not advised	Laboratory No:	C17/3810	
Job Location:	McLeans Island	Report No:	257833	Final
Material:	Pit Run	Report Date:	15/12/2017	Page 1 of 2
Material Source:	McLeans Island			

Test Methods: 1# Sampling from stockpiles of well graded aggregate - machine method NZS4407:2015 2.4.6.3.2
 2 Determination of the Dry Density/Water Content Relationship - New Zealand Vibrating Hammer Compaction Test NZS4402:1986 Test 4.1.3
 # Test methods marked with a hash are not accredited.

Results

Water Content (%)	1.08	2.02	2.53	2.93	3.52	3.94
Dry Density (t/m ³)	2.26	2.27	2.25	2.31	2.27	2.28

Dry Density/Water Content Relationship

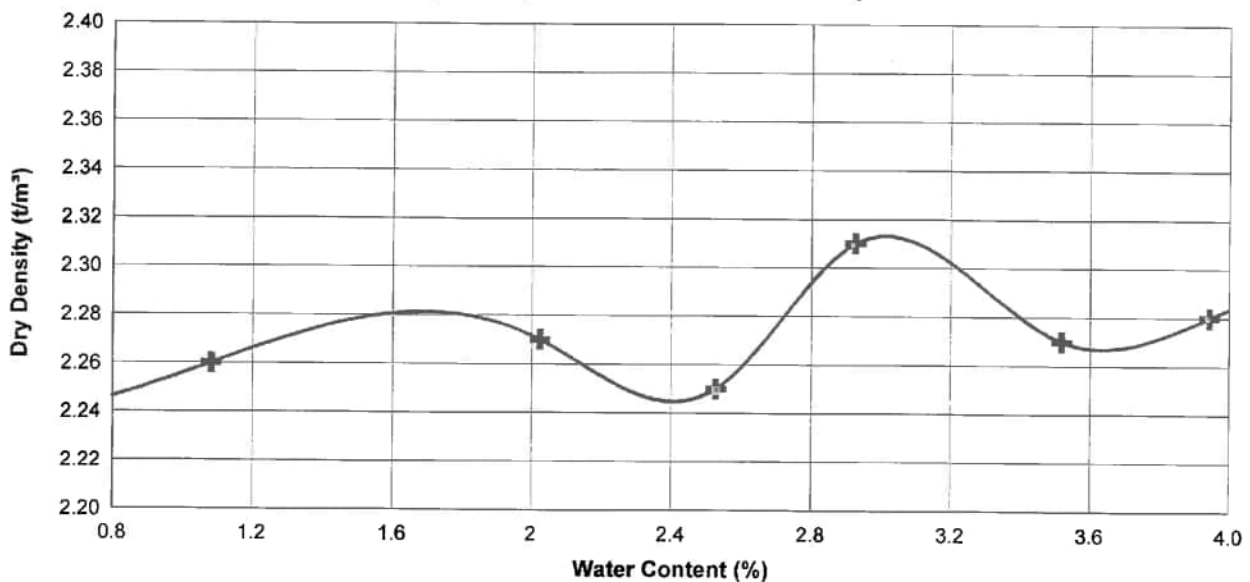

Maximum Dry Density (t/m ³)	2.32
Optimum Water Content (%)	3.0
History of Sample	Result obtained from oven-dried sample.
Test Fraction	Passing 37.5mm sieve
Test Date:	13/12/2017

Notes

Date of sample receipt: 08/12/2017

Vicky Henderson
Approved Signatory
Laboratory Manager
IANZ Accreditation No: 439
Date of Issue: 10/04/92



Tests indicated as not accredited are outside the scope of the laboratory's accreditation.
This report may not be reproduced except in full.

Test Report

Client:	K.B. Contracting & Quarries Limited	Sample Date:	14/10/2021	10:00
Address:	PO Box 19746, Woolston, Christchurch 8241	Sampled By:	Pete Haward	
Job Location:	McLeans Island	Laboratory No:	C21/1895	
Material:	Pitrun	Client Ref:	Not Advised	
Material Source:	McLeans Island	Report No:	52897	Final
		Report Date:	20/10/2021	

Test Methods


- | | | |
|---|--|-----------------------------|
| 1 | Determination of the dry density/water content relationship - New Zealand vibrating hammer compaction test | NZS4402:1986 Test 4.1.3 |
| 2 | Sampling from stockpiles of well graded aggregate - machine method | NZS4407:2015 Test 2.4.6.3.2 |

Determination of the Dry Density/Water Content Relationship - New Zealand Vibrating Hammer Compaction Test

Results

Dry Density (t/m ³)	2.24	2.36	2.33	2.30
Water Content (%)	2.7	4.0	5.3	6.4

Dry Density/Water Content Relationship

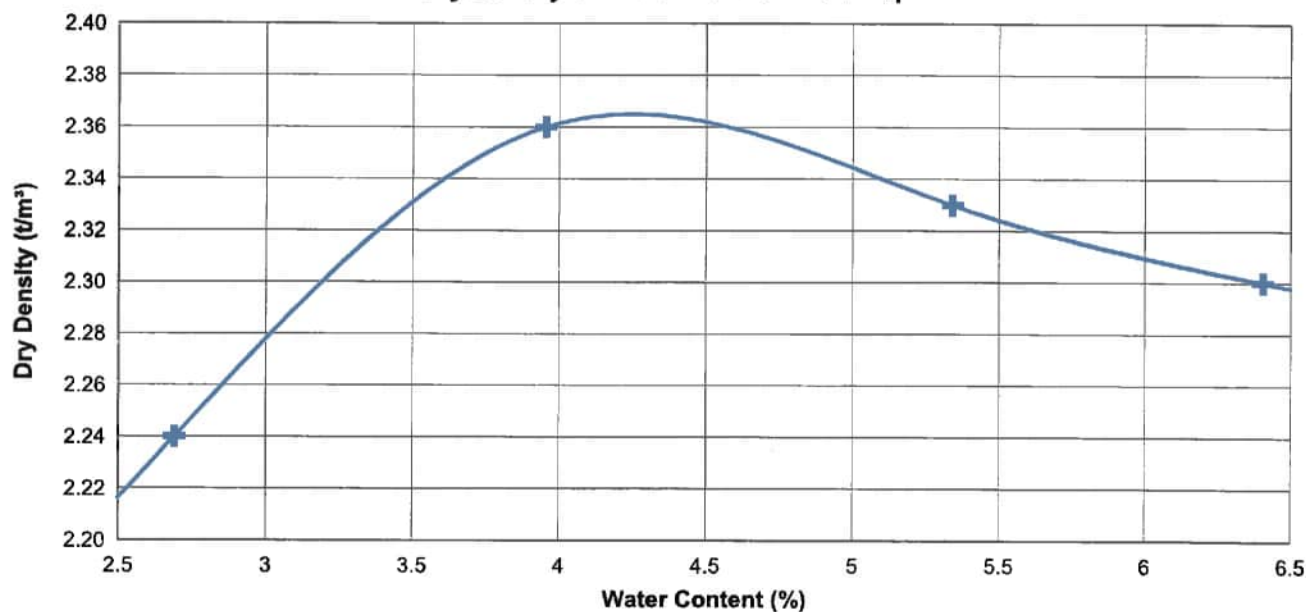

Results

Natural moisture content (%)	3.5
Maximum Dry Density (t/m³)	2.36
Optimum Water Content (%)	4.2
Test Fraction	Passing 37.5mm sieve
Test Date:	19-10-2021

Laboratory No: C21/1895
Report No: 52897
Report Date: 20/10/2021

Final

Sample Notes

Sample received in a damp condition.

Test results apply to sample as received.

Date of sample receipt: 14/10/2021

Vicky Henderson
Laboratory Manager



This report may not be reproduced
except in full.

Test Report

Client: K.B. Contracting & Quarries Limited
Address: PO Box 19746, Woolston, Christchurch 8241
Client Ref: Not Advised
Job Location: Mcleans Island
Material: Pitrun
Material Source: Mcleans Island

Sample Date: 19/04/2021 13:00
Sampled By: Pete Haward
Laboratory No: C21/0839
Report No: 45807 **Final**
Report Date: 27/04/2021

Test Methods

- | | | |
|---|--|-----------------------------|
| 1 | The clay index | NZS 4407:2015 Test 3.5 |
| 2 | Particle size distribution - Subsidiary method by dry sieving | NZS 4407:2015 Test 3.8.2 |
| 3 | Determination of the dry density/water content relationship - New Zealand vibrating hammer compaction test | NZS4402:1986 Test 4.1.3 |
| 4 | * Sampling from stockpiles of well graded aggregate - machine method | NZS4407:2015 Test 2.4.6.3.2 |
- * Test methods marked with an asterisk are not accredited.

The Clay Index

Results

Clay Index: 1.9
Test Date: 23-04-2021


Note: The field sample was sourced from natural fines

Determination of the Dry Density/Water Content Relationship - New Zealand Vibrating Hammer Compaction Test

Results

Dry Density (t/m ³)	2.25	2.37	2.37	2.34	2.27
Water Content (%)	3.2	4.3	5.1	5.4	7.0

Dry Density/Water Content Relationship

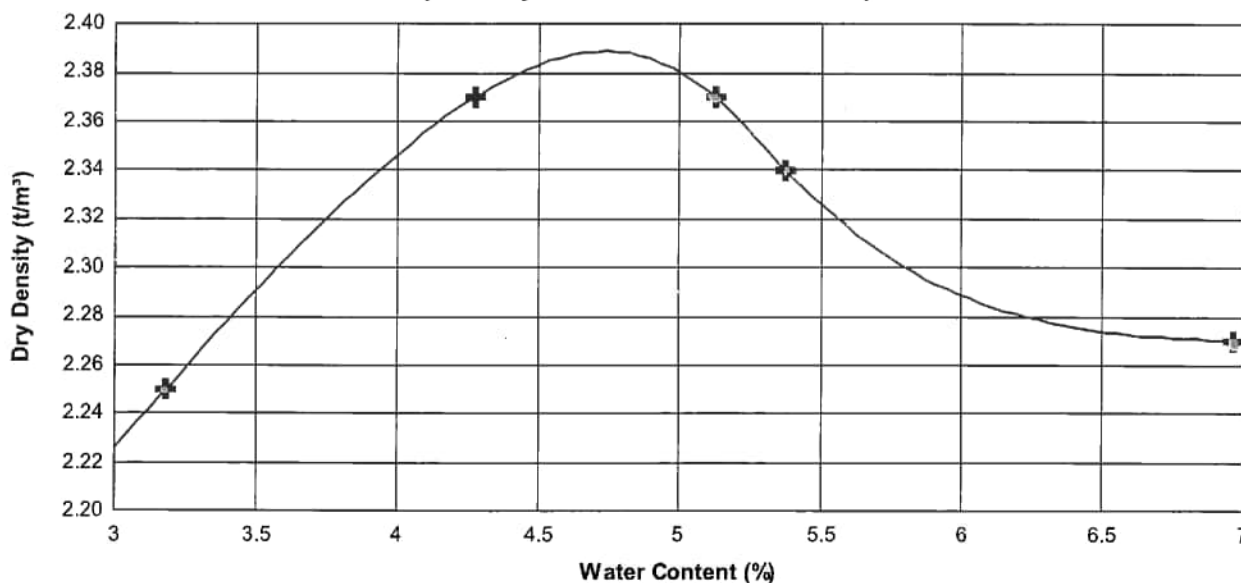

Laboratory No: C21/0839
Report No: 45807
Report Date: 27/04/2021

Final


Results

Maximum Dry Density (t/m³) 2.38
Optimum Water Content (%) 4.8
Test Fraction Passing 37.5mm sieve
Test Date: 20-04-2021

The Particle-Size Distribution - Subsidiary Method by Dry Sieving

Results

Sieve Size (BSS)	Percent passing	Specification
150mm	100	
125mm	95	
106mm	95	
75.0mm	89	
63.0mm	87	
53.0mm	83	
37.5mm	74	
26.5mm	61	
19.0mm	50	
13.2mm	38	
9.5mm	30	
6.7mm	24	
4.75mm	19	
2.36mm	14	
1.18mm	12	
600µm	11	
300µm	7	
150µm	2	
75µm	0	

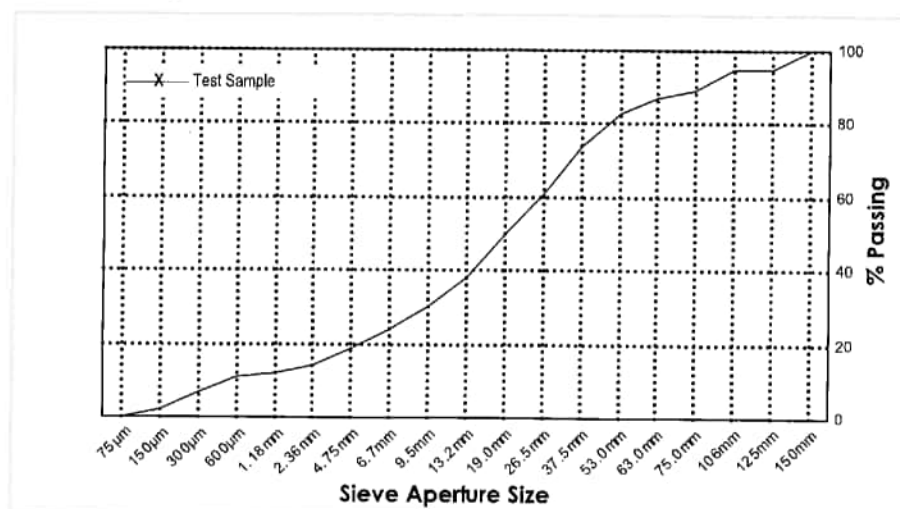

Note: PSD results obtained from an oven dry test sample.

Test Date: 27-04-2021

Sample Notes

Sample received in a damp condition.

Test results apply to sample as received.

Date of sample receipt: 20/04/2021

Vicky Henderson
Approved Signatory
Laboratory Manager
IANZ Accreditation No: 439



Tests indicated as not accredited are outside the scope of the laboratory's accreditation. This report may not be reproduced except in full.



Appendix C

NDM Earthfill Testing Results

Project Prestons South Subdivision
Project No. 235361

Title Summary of Compaction

Test Date	Test ID#	Test #	Unique ID	mE	mN	Stage	MDD	Type	Lift #	Lot ID	Compaction (%)
19/09/2019	2334/19	5	11	395799.532	812147.449	Stage 5	2320	Pitrun	Lift 1	Lot 1040	100
19/09/2019	2334/19	6	12	395810.316	812129.671	Stage 5	2320	Pitrun	Lift 1	Lot 1040	100
19/09/2019	2334/19	7	13	395818.33	812130.108	Stage 5	2320	Pitrun	Lift 1	Lot 1039	101
19/09/2019	2334/19	8	14	395826.782	812149.489	Stage 5	2320	Pitrun	Lift 1	Lot 1039	101
19/09/2019	2334/19	9	15	395833.923	812149.926	Stage 5	2320	Pitrun	Lift 1	Lot 1038	99
19/09/2019	2334/19	10	16	395845.531	812132.07	Stage 5	2320	Pitrun	Lift 1	Lot 1038	99
19/09/2019	2334/19	11	17	395852.143	812132.841	Stage 5	2320	Pitrun	Lift 1	Lot 1037	99
19/09/2019	2334/19	12	18	395859.194	812151.463	Stage 5	2320	Pitrun	Lift 1	Lot 1037	99
19/09/2019	2334/19	13	19	395868.107	812152.173	Stage 5	2320	Pitrun	Lift 1	Lot 1036	100
19/09/2019	2334/19	14	20	395878.016	812135.998	Stage 5	2320	Pitrun	Lift 1	Lot 1036	97
19/09/2019	2334/19	15	21	395886.759	812136.435	Stage 5	2320	Pitrun	Lift 1	Lot 1035	98
19/09/2019	2334/19	16	22	395894.191	812153.921	Stage 5	2320	Pitrun	Lift 1	Lot 1035	98
25/09/2019	2391/19	1	47	395842.903	812150.659	Stage 5	2320	Pitrun	Lift 2	Lot 1038	98
25/09/2019	2391/19	2	48	395834.969	812131.486	Stage 5	2320	Pitrun	Lift 2	Lot 1038	97
25/09/2019	2391/19	3	49	395827.587	812131.045	Stage 5	2320	Pitrun	Lift 2	Lot 1039	99
25/09/2019	2391/19	4	50	395817.34	812148.675	Stage 5	2320	Pitrun	Lift 2	Lot 1039	99
25/09/2019	2391/19	5	51	395809.296	812148.234	Stage 5	2320	Pitrun	Lift 2	Lot 1040	100
25/09/2019	2391/19	6	52	395800.04	812128.842	Stage 5	2320	Pitrun	Lift 2	Lot 1040	98
24/09/2019	2358/19	1	69	395990.515	812141.585	Stage 5	2320	Pitrun	Lift 1	Lot 1030	100
24/09/2019	2358/19	2	70	395989.204	812157.615	Stage 5	2320	Pitrun	Lift 1	Lot 1030	99
24/09/2019	2358/19	3	71	395967.929	812158.78	Stage 5	2320	Pitrun	Lift 1	Lot 1031	96
24/09/2019	2358/19	4	72	395969.386	812143.043	Stage 5	2320	Pitrun	Lift 1	Lot 1031	101
24/09/2019	2358/19	5	73	395952.191	812141.148	Stage 5	2320	Pitrun	Lift 1	Lot 1032	99
24/09/2019	2358/19	6	74	395950.588	812157.177	Stage 5	2320	Pitrun	Lift 1	Lot 1032	103
24/09/2019	2358/19	7	75	395933.247	812156.303	Stage 5	2320	Pitrun	Lift 1	Lot 1033	97
24/09/2019	2358/19	8	76	395935.287	812140.274	Stage 5	2320	Pitrun	Lift 1	Lot 1033	99
24/09/2019	2358/19	9	77	395907.746	812139.254	Stage 5	2320	Pitrun	Lift 1	Lot 1034	100
24/09/2019	2358/19	10	78	395905.56	812153.972	Stage 5	2320	Pitrun	Lift 1	Lot 1034	101
24/09/2019	2358/19	11	79	395889.239	812153.243	Stage 5	2320	Pitrun	Lift 1	Lot 1035	102
24/09/2019	2358/19	12	80	395890.842	812137.068	Stage 5	2320	Pitrun	Lift 1	Lot 1035	98
24/09/2019	2358/19	13	81	395873.793	812135.757	Stage 5	2320	Pitrun	Lift 1	Lot 1036	98
24/09/2019	2358/19	14	82	395872.627	812151.64	Stage 5	2320	Pitrun	Lift 1	Lot 1036	100
27/09/2019	2382/19	1	83	395990.515	812141.585	Stage 5	2320	Pitrun	Lift 2	Lot 1030	99
27/09/2019	2382/19	2	84	395989.204	812157.615	Stage 5	2320	Pitrun	Lift 2	Lot 1030	97
27/09/2019	2382/19	3	85	395967.929	812158.78	Stage 5	2320	Pitrun	Lift 2	Lot 1031	97
27/09/2019	2382/19	4	86	395969.386	812143.043	Stage 5	2320	Pitrun	Lift 2	Lot 1031	97
27/09/2019	2382/19	5	87	395952.191	812141.148	Stage 5	2320	Pitrun	Lift 2	Lot 1032	99
27/09/2019	2382/19	6	88	395950.588	812157.177	Stage 5	2320	Pitrun	Lift 2	Lot 1032	100
27/09/2019	2382/19	7	89	395933.247	812156.303	Stage 5	2320	Pitrun	Lift 2	Lot 1033	100
27/09/2019	2382/19	8	90	395935.287	812140.274	Stage 5	2320	Pitrun	Lift 2	Lot 1033	97
27/09/2019	2382/19	9	91	395907.746	812139.254	Stage 5	2320	Pitrun	Lift 2	Lot 1034	98
27/09/2019	2382/19	10	92	395905.56	812153.972	Stage 5	2320	Pitrun	Lift 2	Lot 1034	95
27/09/2019	2382/19	11	93	395889.239	812153.243	Stage 5	2320	Pitrun	Lift 2	Lot 1035	96
27/09/2019	2382/19	12	94	395890.842	812137.068	Stage 5	2320	Pitrun	Lift 2	Lot 1035	99

Project Prestons South Subdivision
Project No. 235361

Title Summary of Compaction

Test Date	Test ID#	Test #	Unique ID	mE	mN	Stage	MDD	Type	Lift #	Lot ID	Compaction (%)
27/09/2019	2382/19	13	95	395873.793	812135.757	Stage 5	2320	Pitrun	Lift 2	Lot 1036	96
27/09/2019	2382/19	14	96	395872.627	812151.64	Stage 5	2320	Pitrun	Lift 2	Lot 1036	100
27/09/2019	2382/19	15	97	395855.455	812150.734	Stage 5	2320	Pitrun	Lift 2	Lot 1037	96
27/09/2019	2382/19	16	98	395856.628	812133.306	Stage 5	2320	Pitrun	Lift 2	Lot 1037	98
2/10/2019	2425/19	1	99	395928.637	812155.737	Stage 5	2320	Pitrun	Lift 3	Lot 1033	99
2/10/2019	2425/19	2	100	395940.206	812140.862	Stage 5	2320	Pitrun	Lift 3	Lot 1033	98
2/10/2019	2425/19	3	101	395946.046	812141.082	Stage 5	2320	Pitrun	Lift 3	Lot 1032	99
2/10/2019	2425/19	4	102	395955.412	812157.61	Stage 5	2320	Pitrun	Lift 3	Lot 1032	99
2/10/2019	2425/19	5	103	395962.244	812158.271	Stage 5	2320	Pitrun	Lift 3	Lot 1031	96
2/10/2019	2425/19	6	104	395973.703	812143.837	Stage 5	2320	Pitrun	Lift 3	Lot 1031	98
2/10/2019	2425/19	7	105	395983.069	812139.319	Stage 5	2320	Pitrun	Lift 3	Lot 1030	99
2/10/2019	2425/19	8	106	395994.969	812158.712	Stage 5	2320	Pitrun	Lift 3	Lot 1030	100
3/10/2019	2454/19	3	109	395800.04	812128.842	Stage 5	2320	Pitrun	Final Lift	Lot 1040	95
3/10/2019	2454/19	4	110	395809.296	812148.234	Stage 5	2320	Pitrun	Final Lift	Lot 1040	96
3/10/2019	2454/19	5	111	395817.34	812148.675	Stage 5	2320	Pitrun	Final Lift	Lot 1039	100
3/10/2019	2454/19	6	112	395827.587	812131.045	Stage 5	2320	Pitrun	Final Lift	Lot 1039	99
3/10/2019	2454/19	7	113	395834.969	812131.486	Stage 5	2320	Pitrun	Final Lift	Lot 1038	99
3/10/2019	2454/19	8	114	395842.903	812150.659	Stage 5	2320	Pitrun	Final Lift	Lot 1038	98
3/10/2019	2454/19	9	115	395850.739	812150.694	Stage 5	2320	Pitrun	Final Lift	Lot 1037	96
3/10/2019	2454/19	10	116	395862.259	812133.451	Stage 5	2320	Pitrun	Final Lift	Lot 1037	100
3/10/2019	2454/19	11	117	395867.982	812134.9	Stage 5	2320	Pitrun	Final Lift	Lot 1036	97
3/10/2019	2454/19	12	118	395876.966	812152.36	Stage 5	2320	Pitrun	Final Lift	Lot 1036	97
3/10/2019	2454/19	13	119	395885.152	812152.795	Stage 5	2320	Pitrun	Final Lift	Lot 1035	98
3/10/2019	2454/19	14	120	395896.527	812137.218	Stage 5	2320	Pitrun	Final Lift	Lot 1035	103
3/10/2019	2454/19	15	121	395903.468	812137.635	Stage 5	2320	Pitrun	Final Lift	Lot 1034	102
3/10/2019	2454/19	16	122	395911.324	812154.69	Stage 5	2320	Pitrun	Final Lift	Lot 1034	99
3/10/2019	2454/19	17	123	395928.637	812155.737	Stage 5	2320	Pitrun	Final Lift	Lot 1033	99
3/10/2019	2454/19	18	124	395940.206	812140.862	Stage 5	2320	Pitrun	Final Lift	Lot 1033	100
3/10/2019	2454/19	19	125	395946.046	812141.082	Stage 5	2320	Pitrun	Final Lift	Lot 1032	100
3/10/2019	2454/19	20	126	395955.412	812157.61	Stage 5	2320	Pitrun	Final Lift	Lot 1032	96
3/10/2019	2454/19	21	127	395962.244	812158.271	Stage 5	2320	Pitrun	Final Lift	Lot 1031	97
3/10/2019	2454/19	22	128	395973.703	812143.837	Stage 5	2320	Pitrun	Final Lift	Lot 1031	98
3/10/2019	2454/19	23	129	395983.069	812139.319	Stage 5	2320	Pitrun	Final Lift	Lot 1030	102
3/10/2019	2454/19	24	130	395994.969	812158.712	Stage 5	2320	Pitrun	Final Lift	Lot 1030	99
12/05/2020	KB20/0149	1	131	395984.608	812125.176	Stage 5	2320	Pitrun	Lift 1	Lot 1029	99
12/05/2020	KB20/0149	2	132	395999.928	812127.83	Stage 5	2320	Pitrun	Lift 1	Lot 1029	98
12/05/2020	KB20/0149	3	133	396001.897	812110.027	Stage 5	2320	Pitrun	Lift 1	Lot 1028	99
12/05/2020	KB20/0149	4	134	395987.261	812108.829	Stage 5	2320	Pitrun	Lift 1	Lot 1028	100
13/05/2020	KB20/0158	1	139	395999.928	812127.83	Stage 5	2320	Pitrun	Lift 2	Lot 1029	100
13/05/2020	KB20/0158	2	140	396001.897	812110.027	Stage 5	2320	Pitrun	Lift 2	Lot 1028	101
13/05/2020	KB20/0158	7	145	395987.261	812108.829	Stage 5	2320	Pitrun	Lift 2	Lot 1028	99
13/05/2020	KB20/0158	8	146	395984.608	812125.176	Stage 5	2320	Pitrun	Lift 2	Lot 1029	98
19/11/2020	1949-20	1	167	395935.703	812110.221	Stage 5	1600	Sand	Lift 3	Lot 1004	103
19/11/2020	1949-20	2	168	395927.704	812094.098	Stage 5	1600	Sand	Lift 3	Lot 1004	100

Project Prestons South Subdivision
Project No. 235361

Title Summary of Compaction

Test Date	Test ID#	Test #	Unique ID	mE	mN	Stage	MDD	Type	Lift #	Lot ID	Compaction (%)
16/11/2020	1922-20	1	171	395925.713	812109.725	Stage 5	1600	Sand	Lift 2	Lot 1004	98
16/11/2020	1922-20	2	172	395938.786	812094.369	Stage 5	1600	Sand	Lift 2	Lot 1004	100
16/11/2020	1922-20	7	177	395927.052	812094.013	Stage 5	1600	Sand	Lift 2	Lot 1004	101
16/11/2020	1922-20	8	178	395936.267	812110.445	Stage 5	1600	Sand	Lift 2	Lot 1004	99
11/11/2020	1912-20	1	179	395936.34	812109.99	Stage 5	1640	Sand	Lift 1	Lot 1004	98
11/11/2020	1912-20	2	180	395927.633	812093.531	Stage 5	1640	Sand	Lift 1	Lot 1004	100
11/11/2020	1912-20	7	185	395927.422	812093.655	Stage 5	1640	Sand	Lift 1	Lot 1004	99
11/11/2020	1912-20	8	186	395936.047	812109.827	Stage 5	1640	Sand	Lift 1	Lot 1004	102
16/11/2020	KB20/0425	1	247	395945.129	812112.472	Stage 5	2320	Pitrun	Lift 1	Lot 1005	98
16/11/2020	KB20/0425	2	248	395946.465	812095.777	Stage 5	2320	Pitrun	Lift 1	Lot 1005	97
17/11/2020	KB20/0426	1	251	395945.267	812111.807	Stage 5	2320	Pitrun	Lift 2	Lot 1005	98
17/11/2020	KB20/0426	2	252	395947.143	812096.107	Stage 5	2320	Pitrun	Lift 2	Lot 1005	99
20/11/2020	KB20/0432	1	255	395951.296	812112.53	Stage 5	2320	Pitrun	Final Lift	Lot 1005	98
20/11/2020	KB20/0432	2	256	395961.24	812099.101	Stage 5	2320	Pitrun	Final Lift	Lot 1005	99
20/01/2022	3071_001 (0051/2	1	328	396010.149	812109.322	Stage 5	2360	Pitrun	Lift 11	Gravel embankment - From Lot 1028 to Lot 1030 in 15 m intervals	95
20/01/2022	3071_001 (0051/2	2	329	396007.881	812126.187	Stage 5	2360	Pitrun	Lift 11	Gravel embankment - From Lot 1028 to Lot 1030 in 15 m intervals	96
20/01/2022	3071_001 (0051/2	3	330	396005.093	812147.666	Stage 5	2360	Pitrun	Lift 11	Gravel embankment - From Lot 1028 to Lot 1030 in 15 m intervals	95
20/01/2022	3071_001 (0051/2	4	331	396002.866	812161.695	Stage 5	2360	Pitrun	Lift 11	Gravel embankment - From Lot 1028 to Lot 1030 in 15 m intervals	95
23/02/2022	KB22/0071	1	400	395811.448	812104.845	Stage 5	2360	Pitrun	Lift 2	Lot 982	96
23/02/2022	KB22/0071	2	401	395824.697	812105.513	Stage 5	2360	Pitrun	Lift 2	Lot 982	99
23/02/2022	KB22/0071	3	402	395854.09	812107.851	Stage 5	2360	Pitrun	Lift 2	Lot 992	95
23/02/2022	KB22/0071	4	403	395868.786	812108.853	Stage 5	2360	Pitrun	Lift 2	Lot 992	100
23/02/2022	KB22/0071	5	404	395880.477	812109.632	Stage 5	2360	Pitrun	Lift 2	Lot 993	99
23/02/2022	KB22/0071	6	405	395894.06	812109.966	Stage 5	2360	Pitrun	Lift 2	Lot 993	101
23/02/2022	KB22/0073	1	406	395811.448	812104.845	Stage 5	2360	Pitrun	Lift 3	Lot 982	101
23/02/2022	KB22/0073	2	407	395824.697	812105.513	Stage 5	2360	Pitrun	Lift 3	Lot 982	100
22/02/2022	KB22/0065	1	408	395811.448	812104.845	Stage 5	2360	Pitrun	Lift 1	Lot 982	98
22/02/2022	KB22/0065	2	409	395824.697	812105.513	Stage 5	2360	Pitrun	Lift 1	Lot 982	104
22/02/2022	KB22/0065	3	410	395854.09	812107.851	Stage 5	2360	Pitrun	Lift 1	Lot 992	97
22/02/2022	KB22/0065	4	411	395868.786	812108.853	Stage 5	2360	Pitrun	Lift 1	Lot 992	99
22/02/2022	KB22/0065	5	412	395880.477	812109.632	Stage 5	2360	Pitrun	Lift 1	Lot 993	102
22/02/2022	KB22/0065	6	413	395894.06	812109.966	Stage 5	2360	Pitrun	Lift 1	Lot 993	103
24/02/2022	KB22/0080	1	430	395824.697	812105.513	Stage 5	2360	Pitrun	Lift 4	Lot 982	97
24/02/2022	KB22/0080	2	431	395811.448	812104.845	Stage 5	2360	Pitrun	Lift 4	Lot 982	100
7/03/2022	KB22/0096	1	444	395868.786	812108.853	Stage 5	2360	Pitrun	Lift 3	Lot 992	98
7/03/2022	KB22/0096	2	445	395854.09	812107.851	Stage 5	2360	Pitrun	Lift 3	Lot 992	98
30/05/2022	0907_001 (0909/2	7	563	395811.448	812104.845	Stage 5	1560	Sand	Lift 1	Lot 982	102
30/05/2022	0907_001 (0909/2	8	564	395826.876	812088.246	Stage 5	1560	Sand	Lift 1	Lot 982	102
2/06/2022	1022_001 (0939/2	7	571	395811.448	812104.845	Stage 5	1640	Sand	Lift 2	Lot 982	100
2/06/2022	1022_001 (0939/2	8	572	395826.876	812088.246	Stage 5	1640	Sand	Lift 2	Lot 982	104
14/06/2022	1204_001 (1001/2	7	624	395811.448	812104.845	Stage 5	1640	Sand	Lift 3	Lot 982	98
14/06/2022	1204_001 (1001/2	8	625	395826.876	812088.246	Stage 5	1640	Sand	Lift 3	Lot 982	98
17/02/2022	1541_001 (1033/2	7	632	395811.448	812104.845	Stage 5	1640	Sand	Lift 4 (Final)	Lot 982	99
17/02/2022	1541_001 (1033/2	8	633	395826.876	812088.246	Stage 5	1640	Sand	Lift 4 (Final)	Lot 982	99

Project Prestons South Subdivision
Project No. 235361

Title Summary of Compaction

Test Date	Test ID#	Test #	Unique ID	mE	mN	Stage	MDD	Type	Lift #	Lot ID	Compaction (%)
1/10/2019	2421_19 (2454/19	5	666	395799.238	812144.694	Stage 5	2320	Pitrun	lift 3	Lot 1040	98
1/10/2019	2421_19 (2454/19	6	667	395810.003	812133.174	Stage 5	2320	Pitrun	lift 3	Lot 1040	99
1/10/2019	2421_19 (2454/19	7	668	395818.314	812134.352	Stage 5	2320	Pitrun	lift 3	Lot 1039	98
1/10/2019	2421_19 (2454/19	8	669	395826.407	812145.582	Stage 5	2320	Pitrun	lift 3	Lot 1039	101
1/10/2019	2421_19 (2454/19	9	670	395833.464	812146.491	Stage 5	2320	Pitrun	lift 3	Lot 1038	99
1/10/2019	2421_19 (2454/19	10	671	395844.631	812136.063	Stage 5	2320	Pitrun	lift 3	Lot 1038	99
1/10/2019	2421_19 (2454/19	11	672	395850.872	812136.802	Stage 5	2320	Pitrun	lift 3	Lot 1037	101
1/10/2019	2421_19 (2454/19	12	673	395860.56	812148.955	Stage 5	2320	Pitrun	lift 3	Lot 1037	100
1/10/2019	2421_19 (2454/19	13	674	395867.293	812149.283	Stage 5	2320	Pitrun	lift 3	Lot 1036	99
1/10/2019	2421_19 (2454/19	14	675	395879.362	812139.38	Stage 5	2320	Pitrun	lift 3	Lot 1036	99
1/10/2019	2421_19 (2454/19	15	676	395886.255	812139.38	Stage 5	2320	Pitrun	lift 3	Lot 1035	100
1/10/2019	2421_19 (2454/19	16	677	395894.564	812151.277	Stage 5	2320	Pitrun	lift 3	Lot 1035	101
1/10/2019	2421_19 (2454/19	17	678	395900.88	812152.609	Stage 5	2320	Pitrun	lift 3	Lot 1034	97
1/10/2019	2421_19 (2454/19	18	679	395912.117	812140.523	Stage 5	2320	Pitrun	lift 3	Lot 1034	97
27/07/2002	KB22/0286	1	823	396005.503	812142.316	Stage 5	2320	Pit Run	Lift 13	Lot 1030	98
27/07/2002	KB22/0286	2	824	396002.866	812161.695	Stage 5	2320	Pit Run	Lift 13	Lot 1030	98
20/01/2022	KB22/0012	1	875	396010.149	812109.322	Stage 5	2360	Pit Run	Lift 11 - Final	Gravel embankment - From Lot 1028 to Lot 1030 in 15 m intervals	95
20/01/2022	KB22/0012	2	876	396007.881	812126.187	Stage 5	2360	Pit Run	Lift 11 - Final	Gravel embankment - From Lot 1028 to Lot 1030 in 15 m intervals	98
20/01/2022	KB22/0012	3	877	396005.503	812142.316	Stage 5	2360	Pit Run	Lift 11 - Final	Gravel embankment - From Lot 1028 to Lot 1030 in 15 m intervals	95
20/01/2022	KB22/0012	4	878	396002.866	812161.695	Stage 5	2360	Pit Run	Lift 11 - Final	Gravel embankment - From Lot 1028 to Lot 1030 in 15 m intervals	96
13/01/2022	KB22/0002	1	879	396002.866	812161.695	Stage 5	2380	Pit Run	Lift 10	Gravel embankment - From Lot 1030 to Lot 1020 in 15 m intervals	97
13/01/2022	KB22/0002	2	880	396003.439	812154.498	Stage 5	2380	Pit Run	Lift 10	Gravel embankment - From Lot 1030 to Lot 1020 in 15 m intervals	96
13/01/2022	KB22/0002	3	881	396005.503	812142.316	Stage 5	2380	Pit Run	Lift 10	Gravel embankment - From Lot 1030 to Lot 1020 in 15 m intervals	95
13/01/2022	KB22/0002	4	882	396007.881	812126.187	Stage 5	2380	Pit Run	Lift 10	Gravel embankment - From Lot 1030 to Lot 1020 in 15 m intervals	95
13/01/2022	KB22/0002	5	883	396010.149	812109.322	Stage 5	2380	Pit Run	Lift 10	Gravel embankment - From Lot 1030 to Lot 1020 in 15 m intervals	96
13/01/2022	KB22/0002	6	884	396014.613	812086.757	Stage 5	2380	Pit Run	Lift 10	Gravel embankment - From Lot 1030 to Lot 1020 in 15 m intervals	95
13/01/2022	KB22/0002	7	885	396016.628	812071.497	Stage 5	2380	Pit Run	Lift 10	Gravel embankment - From Lot 1030 to Lot 1020 in 15 m intervals	95
13/01/2022	KB22/0002	8	886	396018.075	812056.244	Stage 5	2380	Pit Run	Lift 10	Gravel embankment - From Lot 1030 to Lot 1020 in 15 m intervals	95
13/01/2022	KB22/0002	9	887	396020.367	812039.746	Stage 5	2380	Pit Run	Lift 10	Gravel embankment - From Lot 1030 to Lot 1020 in 15 m intervals	95
13/01/2022	KB22/0002	10	888	396022.528	812022.843	Stage 5	2380	Pit Run	Lift 10	Gravel embankment - From Lot 1030 to Lot 1020 in 15 m intervals	98
13/01/2022	KB22/0002	11	889	396026.729	812013.6	Stage 5	2380	Pit Run	Lift 10	Gravel embankment - From Lot 1030 to Lot 1020 in 15 m intervals	96
13/01/2022	KB22/0002	12	890	396029.526	811998.14	Stage 5	2380	Pit Run	Lift 10	Gravel embankment - From Lot 1030 to Lot 1020 in 15 m intervals	95
13/01/2022	KB22/0002	13	891	396026.287	811983.121	Stage 5	2380	Pit Run	Lift 10	Gravel embankment - From Lot 1030 to Lot 1020 in 15 m intervals	96
13/01/2022	KB22/0002	14	892	396018.63	811970.311	Stage 5	2380	Pit Run	Lift 10	Gravel embankment - From Lot 1030 to Lot 1020 in 15 m intervals	95
13/01/2022	KB22/0001	1	893	396002.735	812163.606	Stage 5	2380	Pit Run	Lift 9	Gravel embankment - From Lot 1030 to Lot 1023	95
13/01/2022	KB22/0001	2	894	396003.439	812154.498	Stage 5	2380	Pit Run	Lift 9	Gravel embankment - From Lot 1030 to Lot 1023	95
13/01/2022	KB22/0001	3	895	396005.856	812139.916	Stage 5	2380	Pit Run	Lift 9	Gravel embankment - From Lot 1030 to Lot 1023	95
13/01/2022	KB22/0001	4	896	396007.881	812126.187	Stage 5	2380	Pit Run	Lift 9	Gravel embankment - From Lot 1030 to Lot 1023	97
13/01/2022	KB22/0001	5	897	396010.149	812109.322	Stage 5	2380	Pit Run	Lift 9	Gravel embankment - From Lot 1030 to Lot 1023	95
13/01/2022	KB22/0001	6	898	396014.613	812086.757	Stage 5	2380	Pit Run	Lift 9	Gravel embankment - From Lot 1030 to Lot 1023	95
13/01/2022	KB22/0001	7	899	396016.628	812071.497	Stage 5	2380	Pit Run	Lift 9	Gravel embankment - From Lot 1030 to Lot 1023	95
13/01/2022	KB22/0001	8	900	396018.075	812056.244	Stage 5	2380	Pit Run	Lift 9	Gravel embankment - From Lot 1030 to Lot 1023	95
13/01/2022	KB22/0001	9	901	396020.367	812039.746	Stage 5	2380	Pit Run	Lift 9	Gravel embankment - From Lot 1030 to Lot 1023	95
13/01/2022	KB22/0001	10	902	396022.528	812022.843	Stage 5	2380	Pit Run	Lift 9	Gravel embankment - From Lot 1030 to Lot 1023	98

Project Prestons South Subdivision
Project No. 235361




Title Summary of Compaction

Test Date	Test ID#	Test #	Unique ID	mE	mN	Stage	MDD	Type	Lift #	Lot ID	Compaction (%)
6/09/2022	1480/22	5	907	395938.786	812094.369			1640 Sand	Lift 4	Lot 1004	99
6/09/2022	1480/22	6	908	395925.713	812109.725			1640 Sand	Lift 4	Lot 1004	96
8/09/2022	KB2/0366	1	909	395895.983	812097.66			2320 Pit Run	Lift 1	Lot 993	100
8/09/2022	KB2/0366	2	910	395882.001	812096.553			2320 Pit Run	Lift 1	Lot 993	102
8/09/2022	KB2/0366	3	911	395869.729	812095.245			2320 Pit Run	Lift 1	Lot 992	101
8/09/2022	KB2/0366	4	912	395855.143	812094.038			2320 Pit Run	Lift 1	Lot 992	99
9/09/2022	KB2/0369	1	913	395895.983	812097.66			2320 Pit Run	Lift 2	Lot 993	96
9/09/2022	KB2/0369	2	914	395882.001	812096.553			2320 Pit Run	Lift 2	Lot 993	98
9/09/2022	KB2/0369	3	915	395869.729	812095.245			2320 Pit Run	Lift 2	Lot 992	97
9/09/2022	KB2/0369	4	916	395855.143	812094.038			2320 Pit Run	Lift 2	Lot 992	97
6/09/2022	1480 (1480/22)	5	937	395927.704	812094.098			1640 Sand	Final Lift	Lot 1004	99
6/09/2022	1480 (1480/22)	6	938	395936.267	812110.445			1640 Sand	Final Lift	Lot 1004	96
13/09/2022	KB22/0375	1	939	395855.143	812094.038			2320 Pit Run	Lift 3	Lot 992	98
13/09/2022	KB22/0375	2	940	395869.729	812095.245			2320 Pit Run	Lift 3	Lot 992	97
13/09/2022	KB22/0375	3	941	395882.001	812096.553			2320 Pit Run	Lift 3	Lot 993	97
13/09/2022	KB22/0375	4	942	395895.983	812097.66			2320 Pit Run	Lift 3	Lot 993	97
13/09/2022	1515 (1515/22)	1	943	395854.09	812107.851			2320 Pit Run	Final Lift	Lot 992	98
13/09/2022	1515 (1515/22)	2	944	395869.729	812095.245			2320 Pit Run	Final Lift	Lot 992	96
13/09/2022	1515 (1515/22)	3	945	395882.001	812096.553			2320 Pit Run	Final Lift	Lot 993	96
13/09/2022	1515 (1515/22)	4	946	395894.06	812109.966			2320 Pit Run	Final Lift	Lot 993	96



Appendix D

Gravel Embankment Design and As-Builts

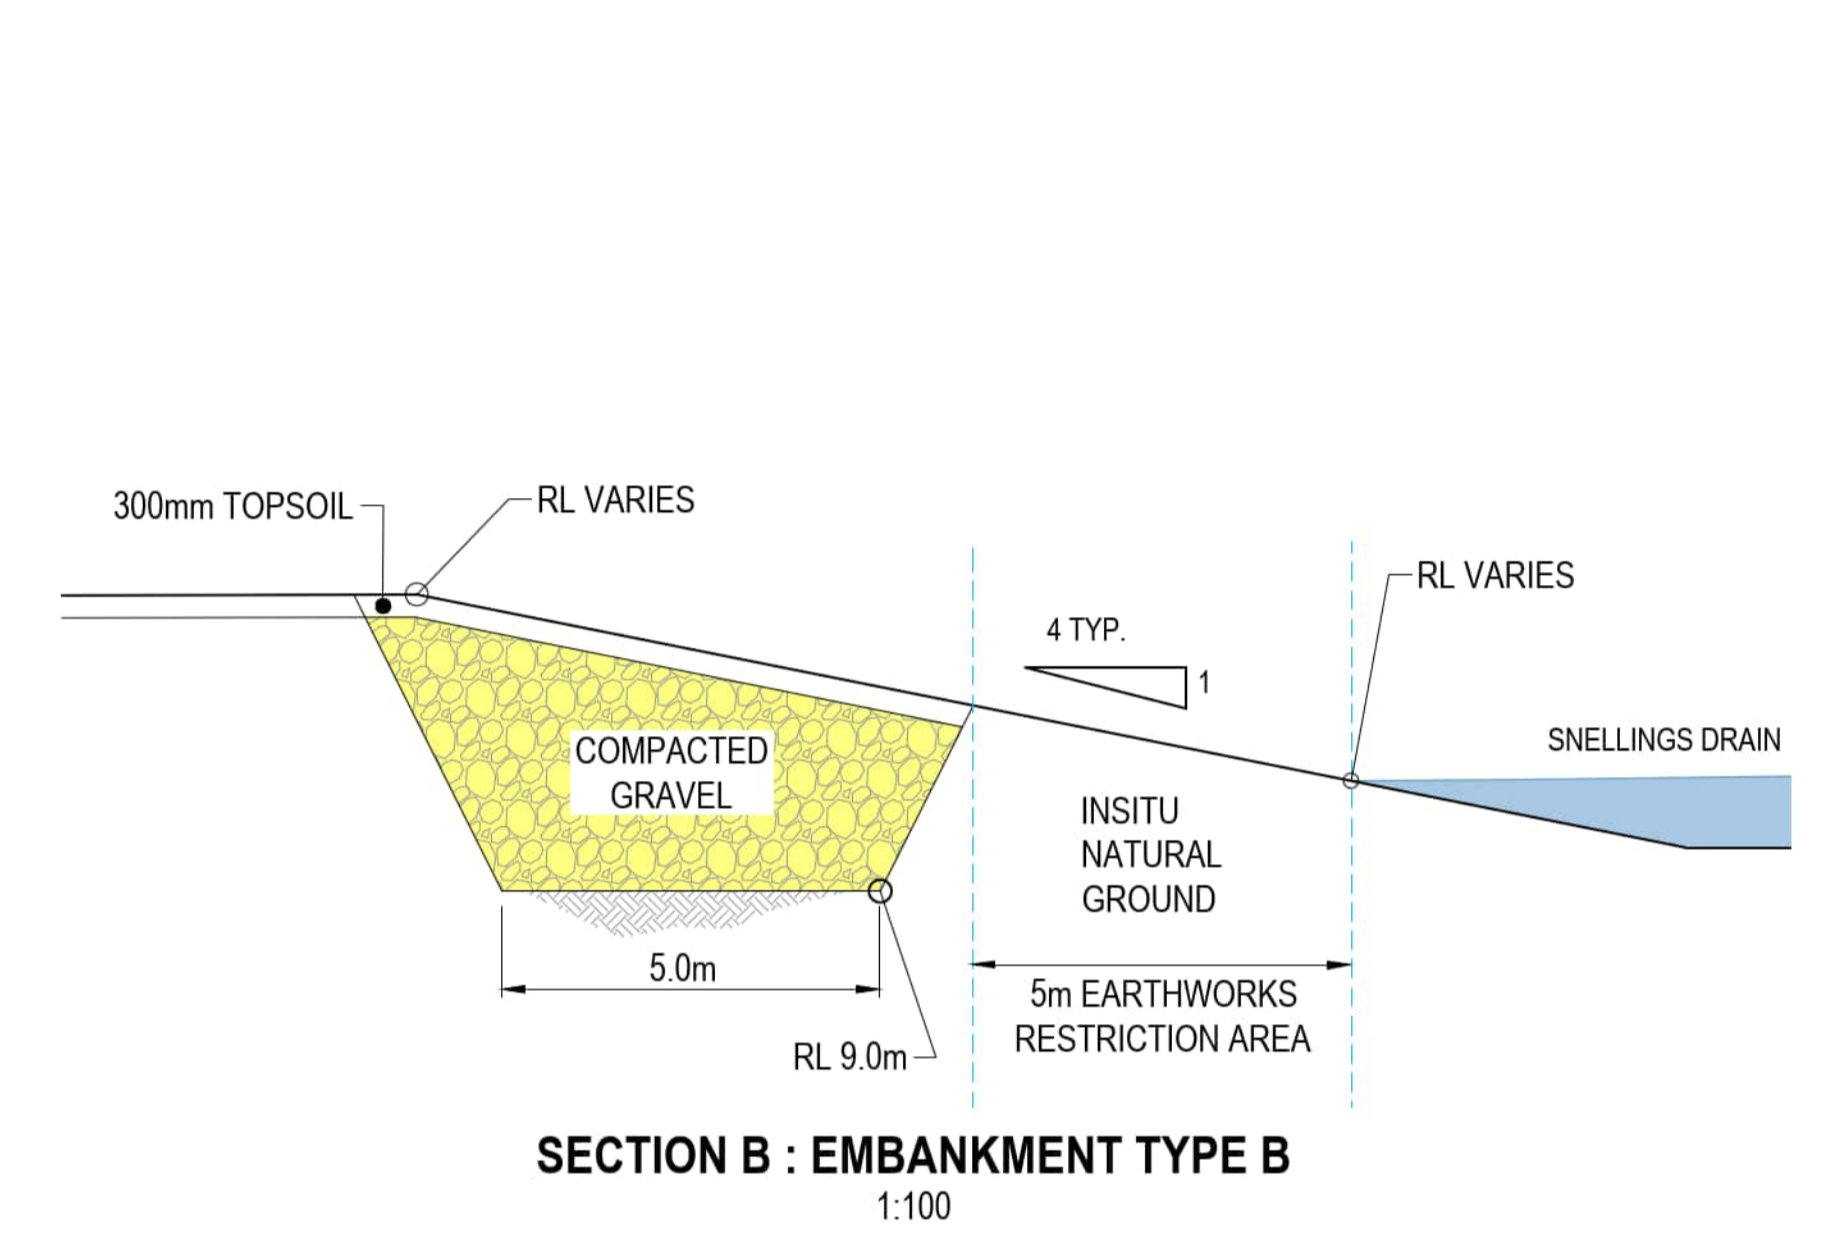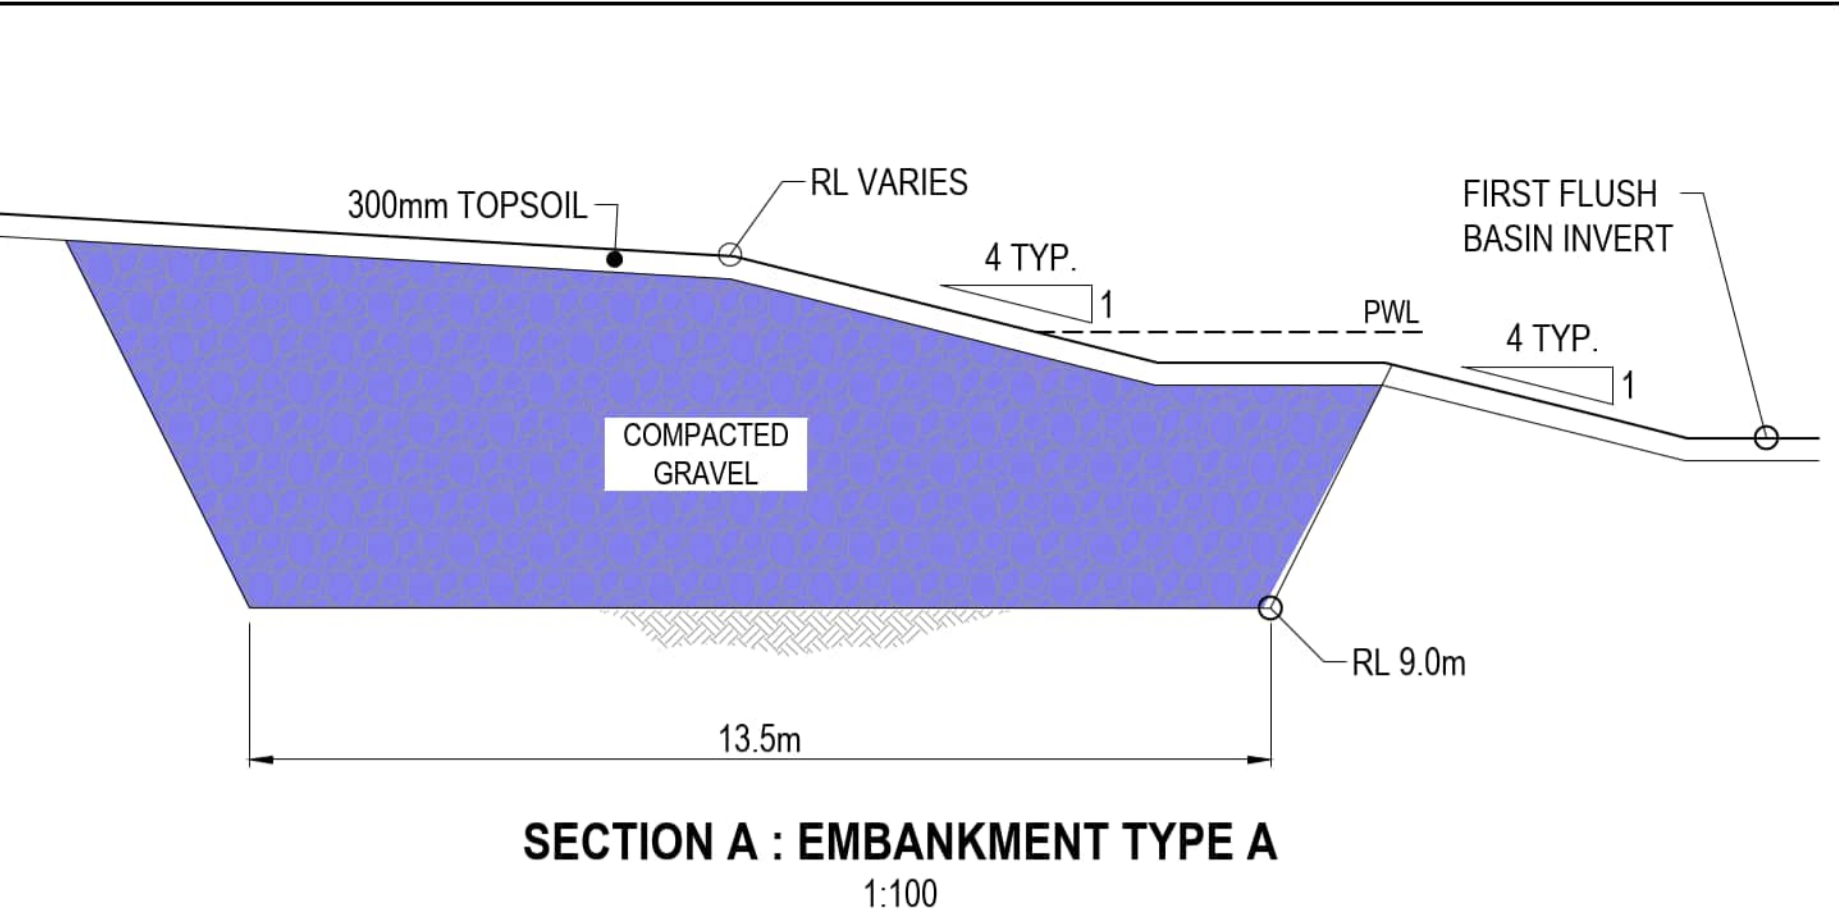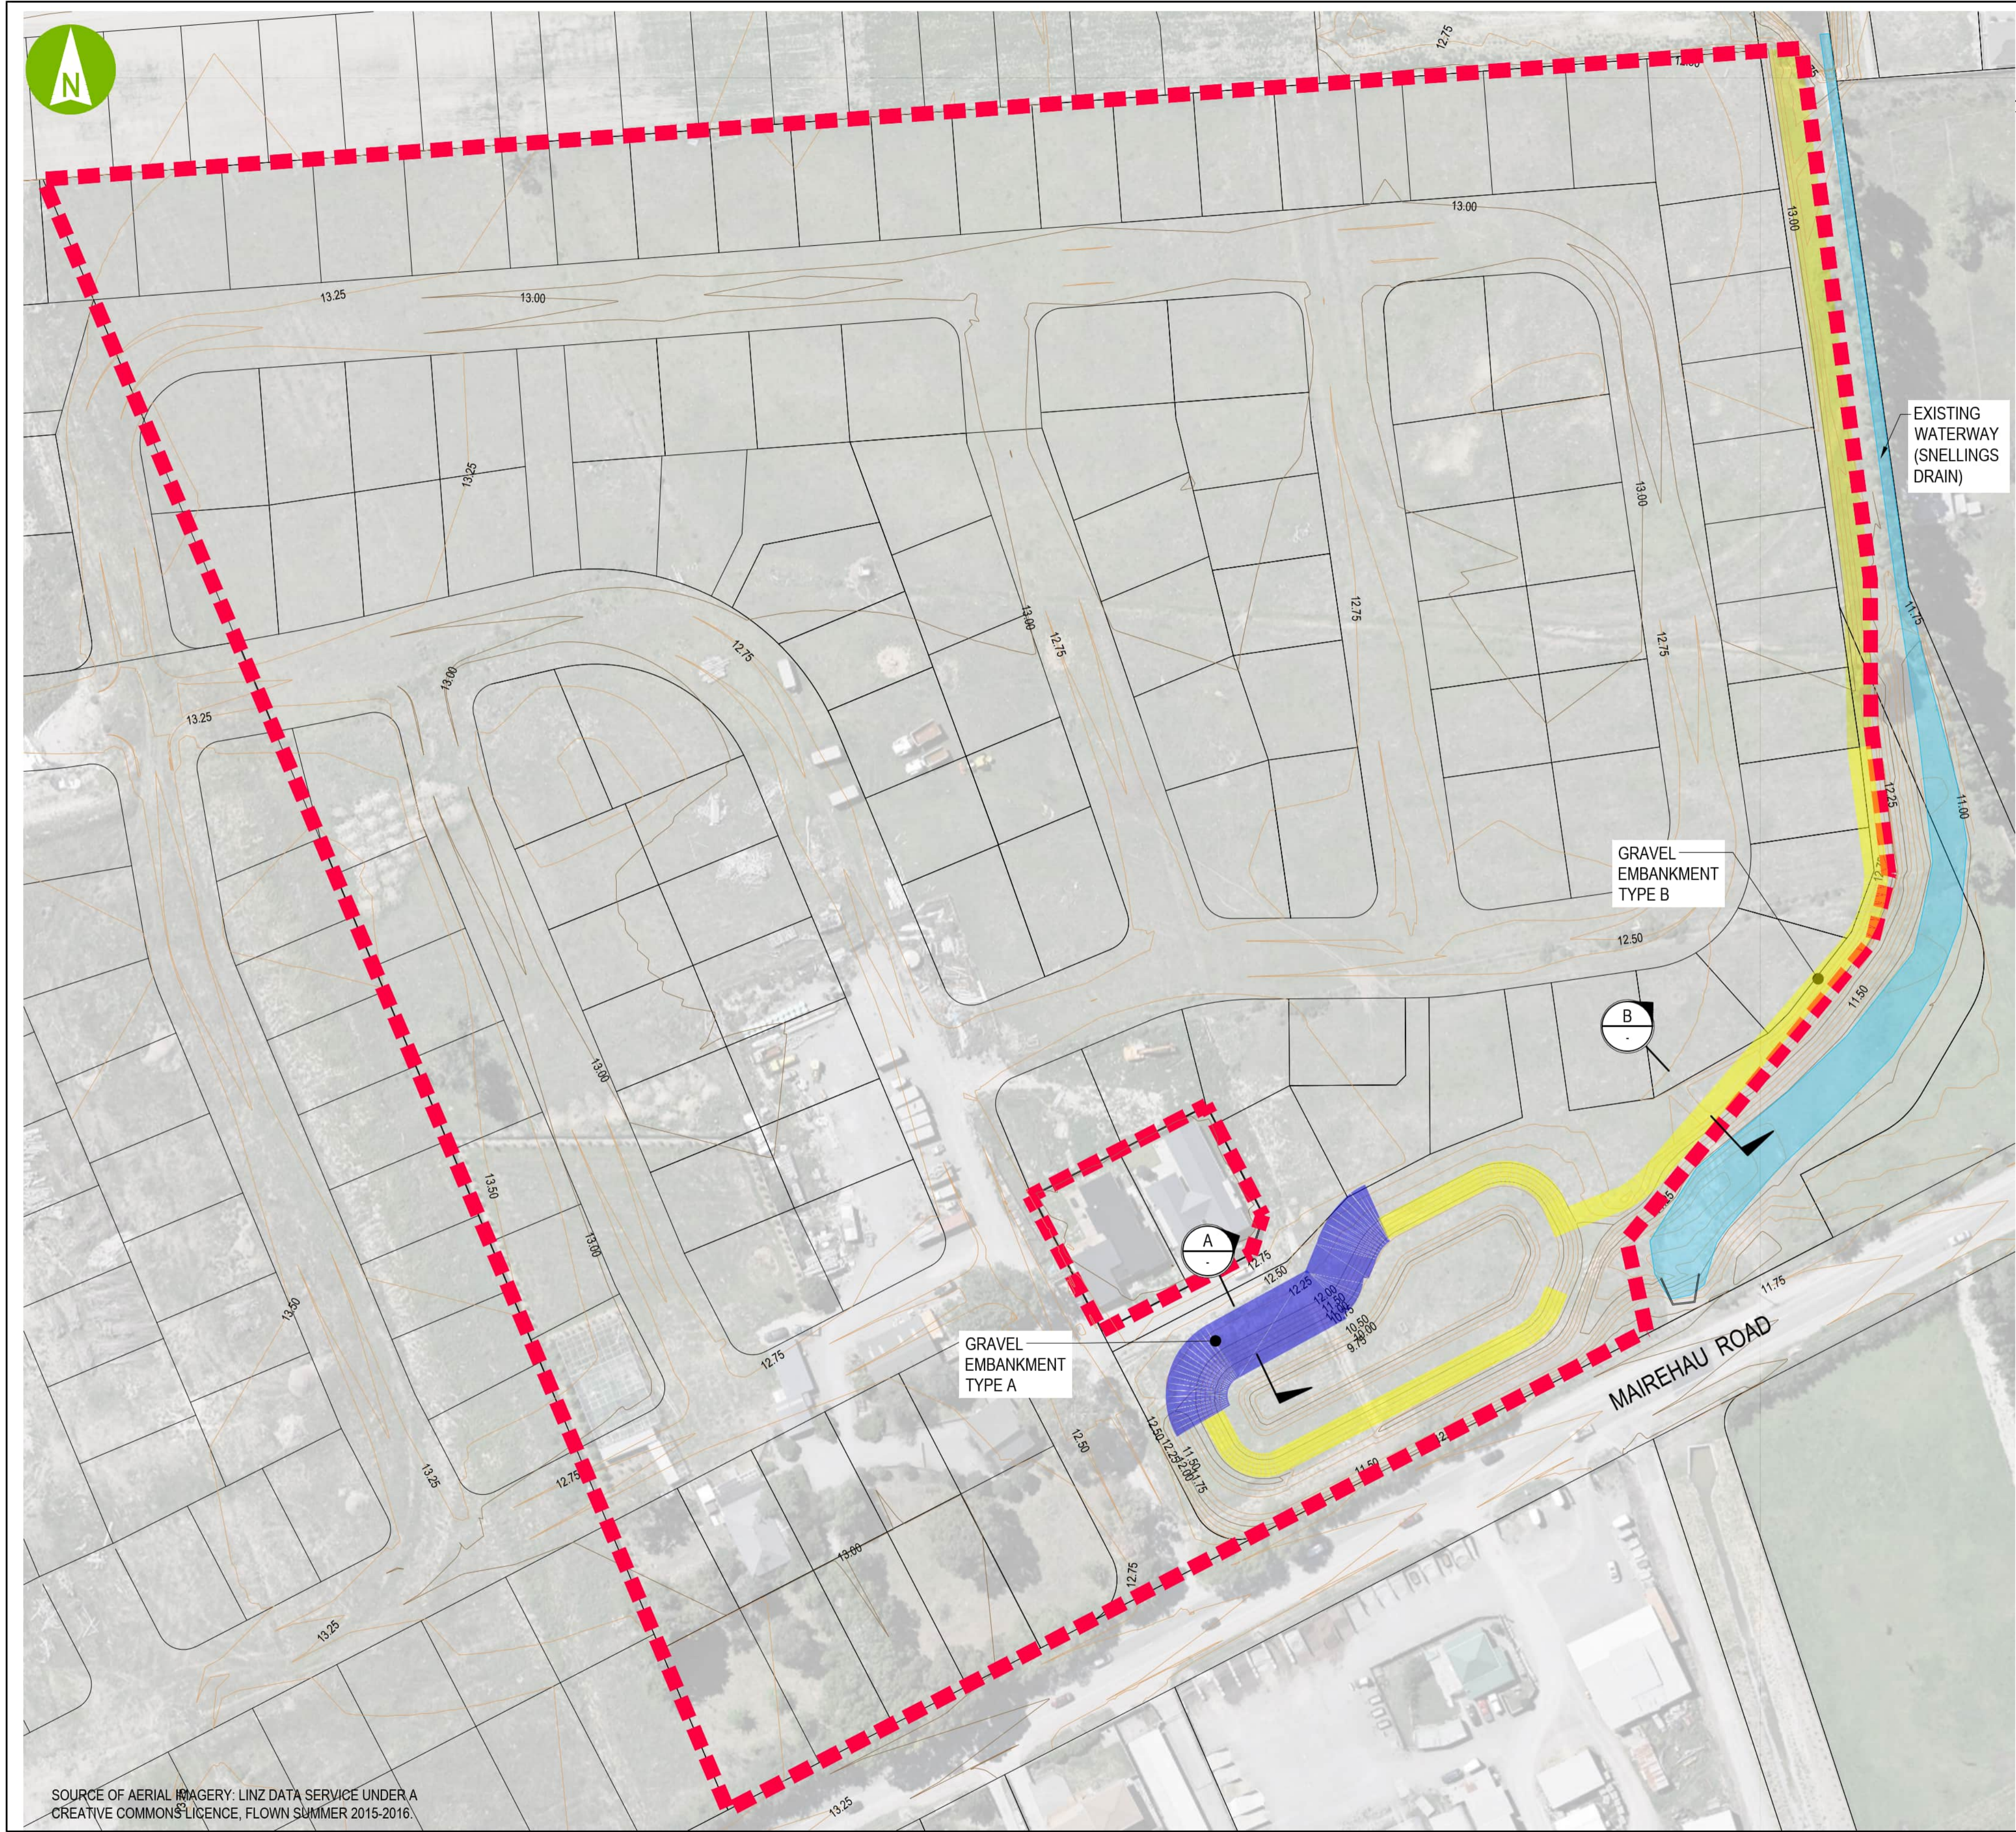

- NOTES
1. NO EARTHWORKS OR WORKS ASSOCIATED WITH EARTHWORKS ARE TO BE UNDERTAKEN IN CCC LAND OR WITHIN 5m OF SNELLINGS DRAIN.
 2. COMPACTED EMBANKMENT GRAVEL TO BE CCC APPROVED AP65 OR PIT RUN. COMPACTION TO BE COMPLETED TO 98% OF THE MAXIMUM DRY DENSITY IN ACCORDANCE WITH NZS4402 TEST 4.1.3.
 3. CUT SUBGRADE TO BE INSPECTED BY SUITABLY QUALIFIED GEOTECHNICAL ENGINEER.
 4. ALL EXCAVATIONS TO BE CARRIED OUT IN ACCORDANCE WITH WORKSAFE AND CCC SAFE TRENCHING GUIDELINES.
 5. INTERNAL BOUNDARIES ARE INDICATIVE ONLY AND ARE SUBJECT TO CHANGE. BOUNDARIES TO BE CONFIRMED AT TIME OF SUBDIVISION CONSENT.
 6. FINAL TOPOGRAPHY OF THE DRAIN AND BASIN VARIES SIGNIFICANTLY ACROSS THE SITE. REFER TO CIVIL DESIGN MODEL FOR FINAL EARTHWORKS FINISHED LEVELS. THIS DRAWING IS TO BE USED FOR DIMENSIONS OF GRAVEL EMBANKMENT ONLY.



REV	DATE	REVISION DETAILS
1	06/09/19	ISSUE FOR CONSTRUCTION
0	27/08/19	ISSUE FOR CONSTRUCTION


APPROVED	DRAWN	DESIGNED
K ASHBY	J W-K	K FOOTE

PROJECT	PRESTONS PARK
TITLE	STAGE 5 EARTHWORKS GRAVEL EMBANKMENT DETAILS


CONSTRUCTION	
PROJECT No.	235361
SCALE	1:750
DRAWING No.	PS-S5-EW-05
SIZE	A1
REV	1




CLIENT		REV	DATE	REVISION DETAILS	APPROVED	DRAWN	DESIGNED	PROJECT		AS BUILT	
						A. COLUMBUS	M. CROWE	PRESTONS PARK		PROJECT No.	
						CHECKED				235361	
						APPROVED		TITLE		SCALE	SIZE
								STAGE 5		1:1000(m)	A1
						DATE		GRAVEL EMBANKMENT		DRAWING No.	REV
								AS BUILT PLAN		LD-PS-S5-EW-12	A
		A	20/10/22	AS BUILT ISSUE							

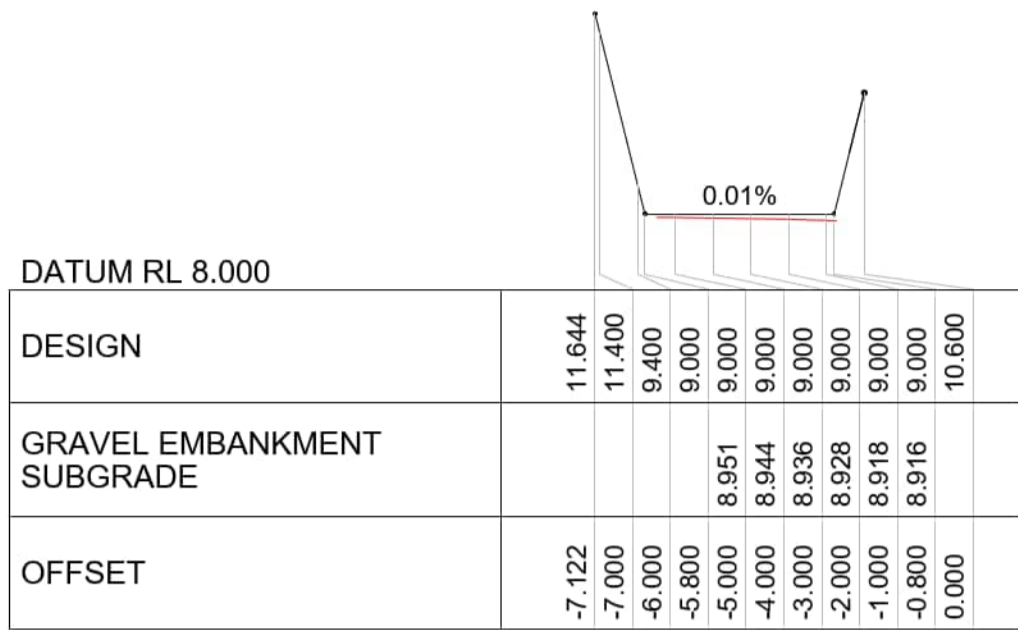


CHAINAGE 60

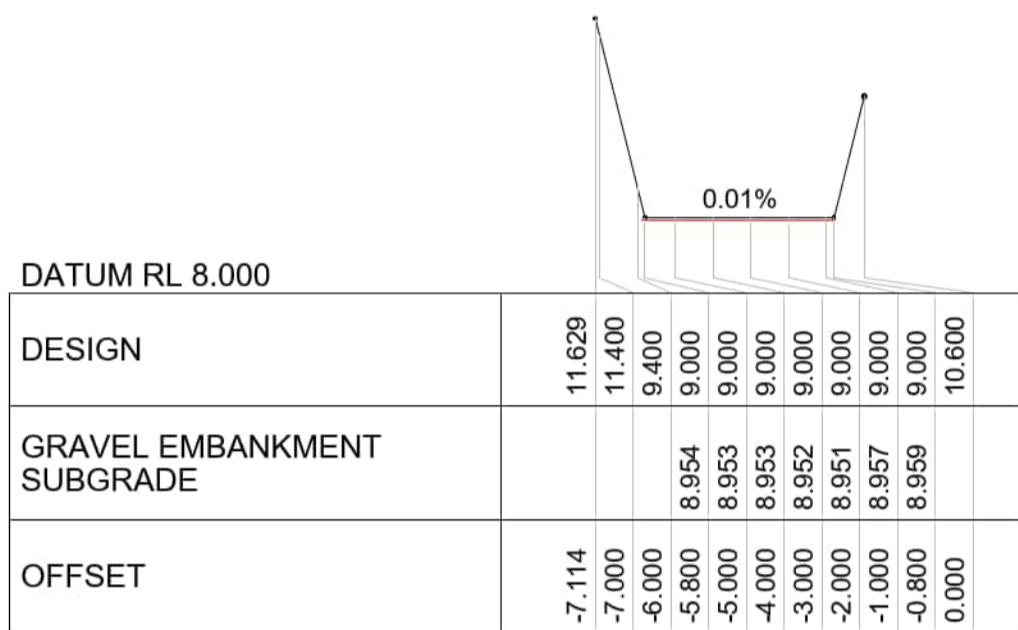


CHAINAGE 40

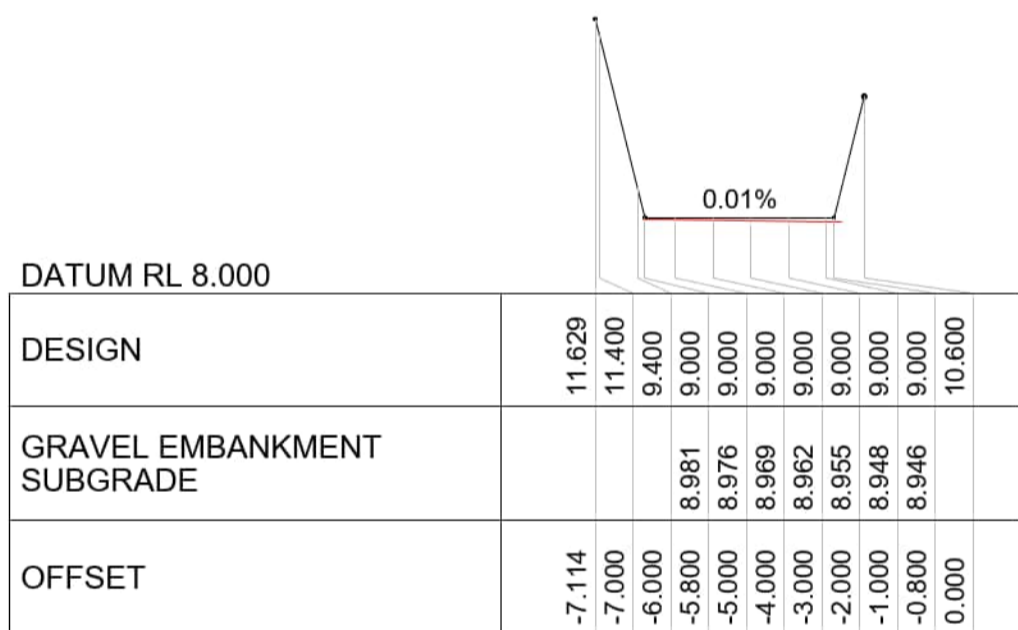


CHAINAGE 20

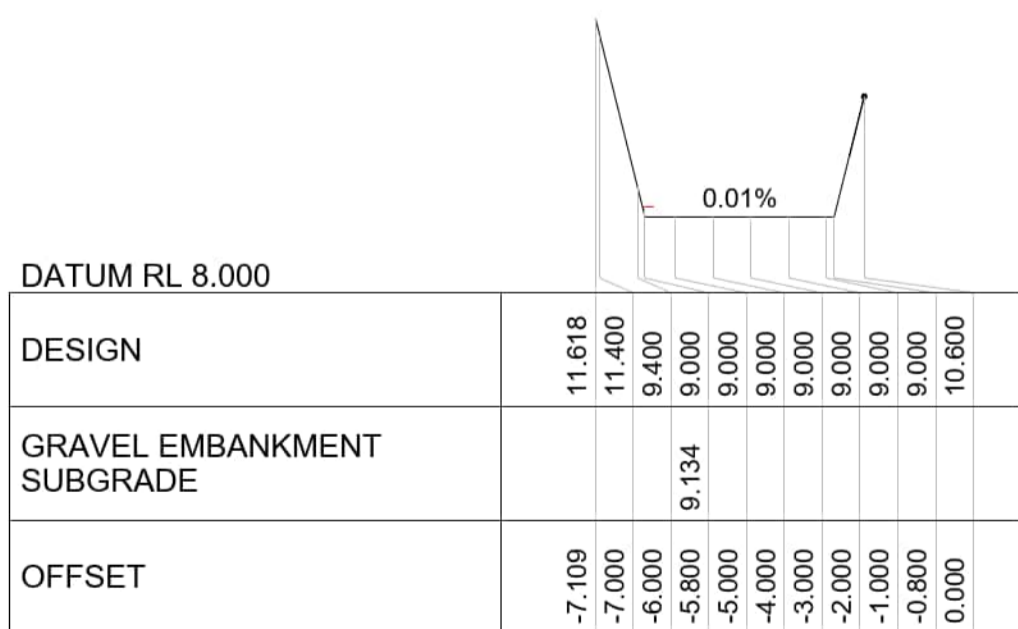


CHAINAGE 0

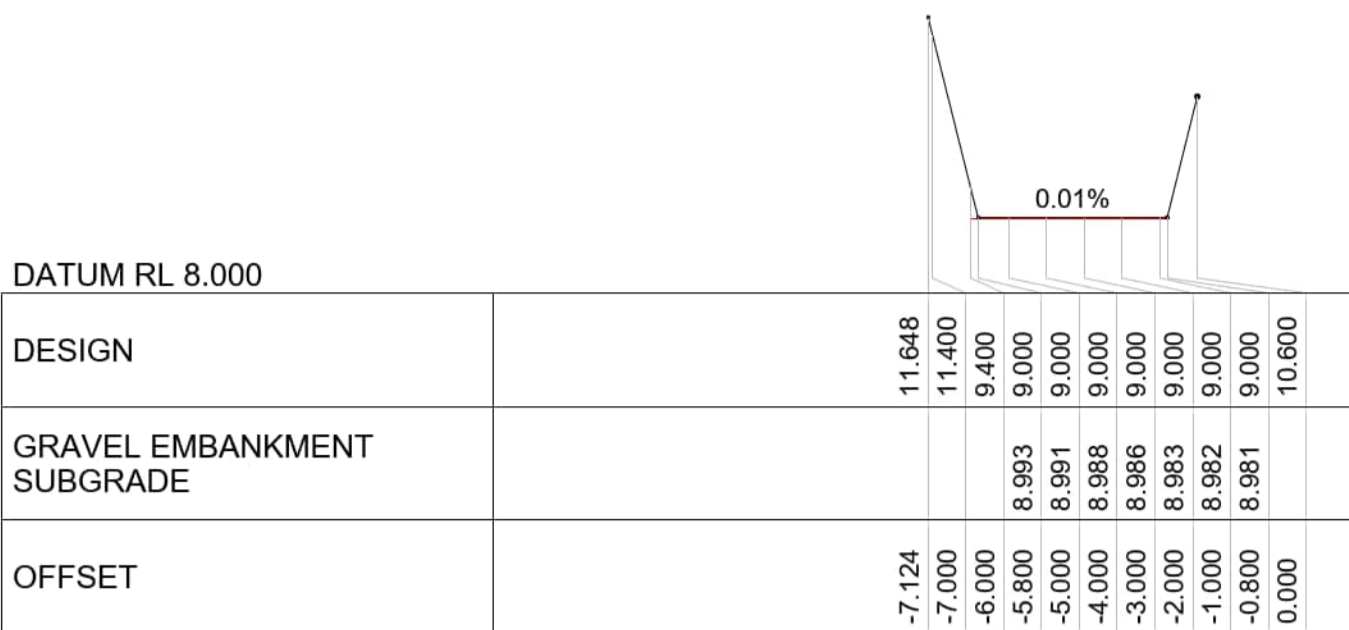


CHAINAGE 140

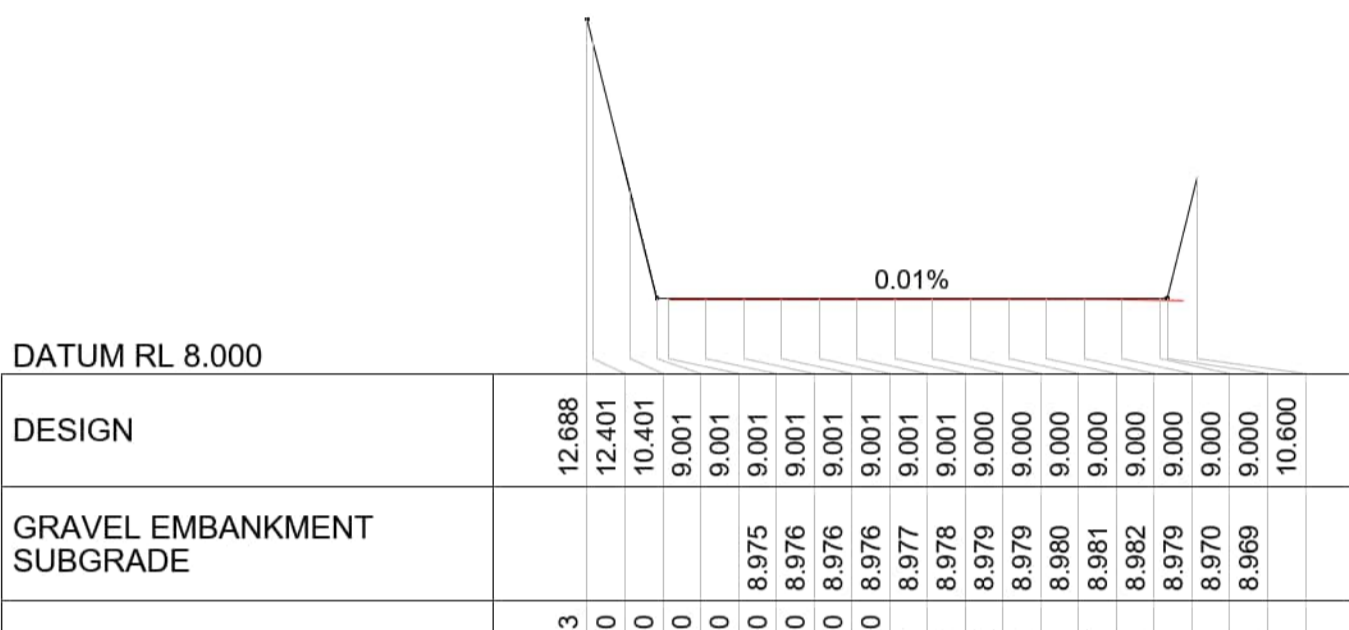


CHAINAGE 120

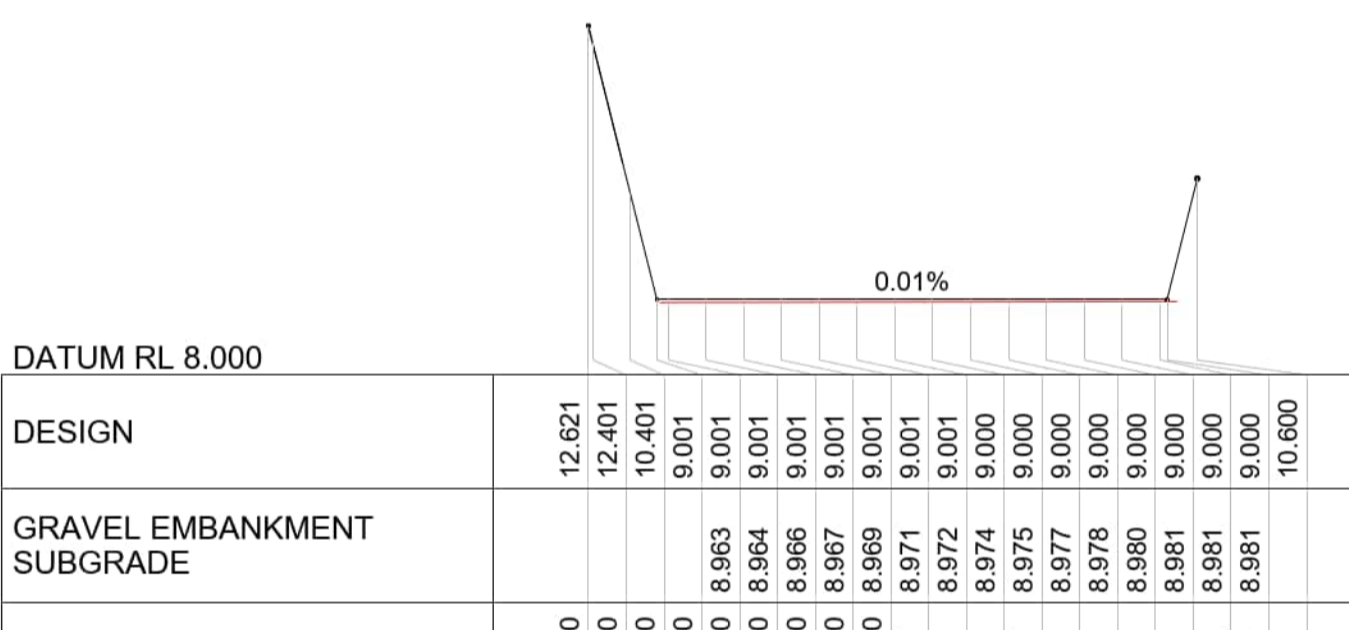


CHAINAGE 100

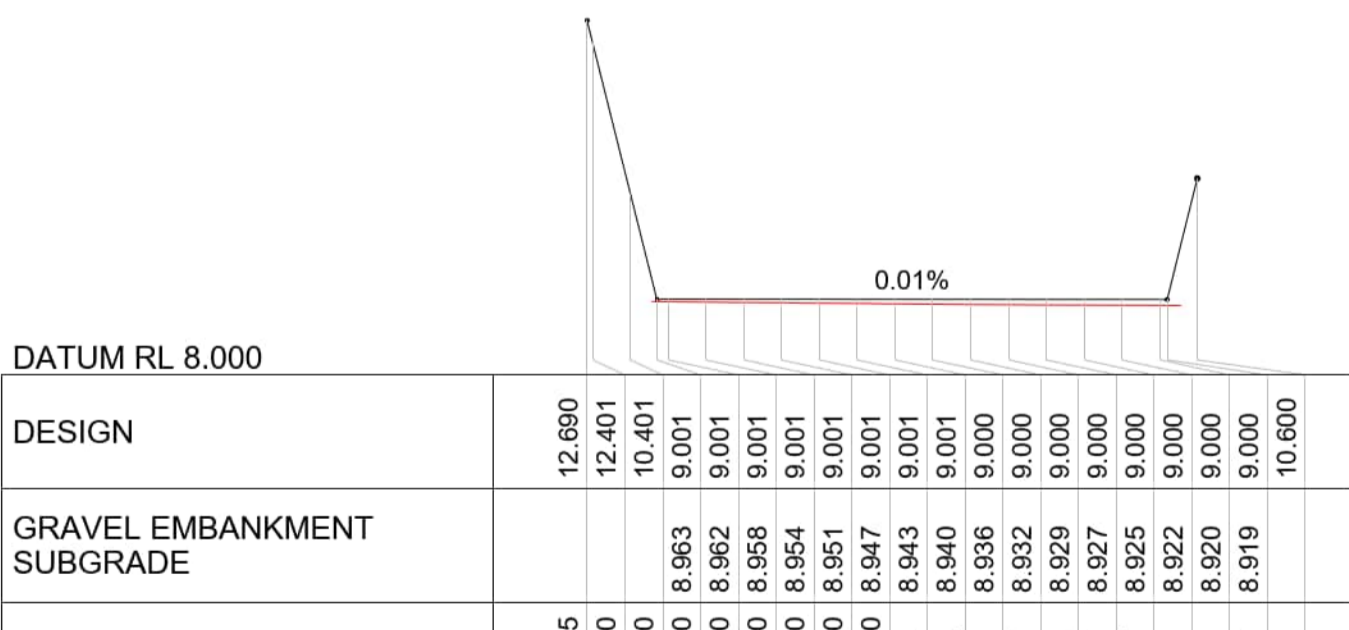


CHAINAGE 80

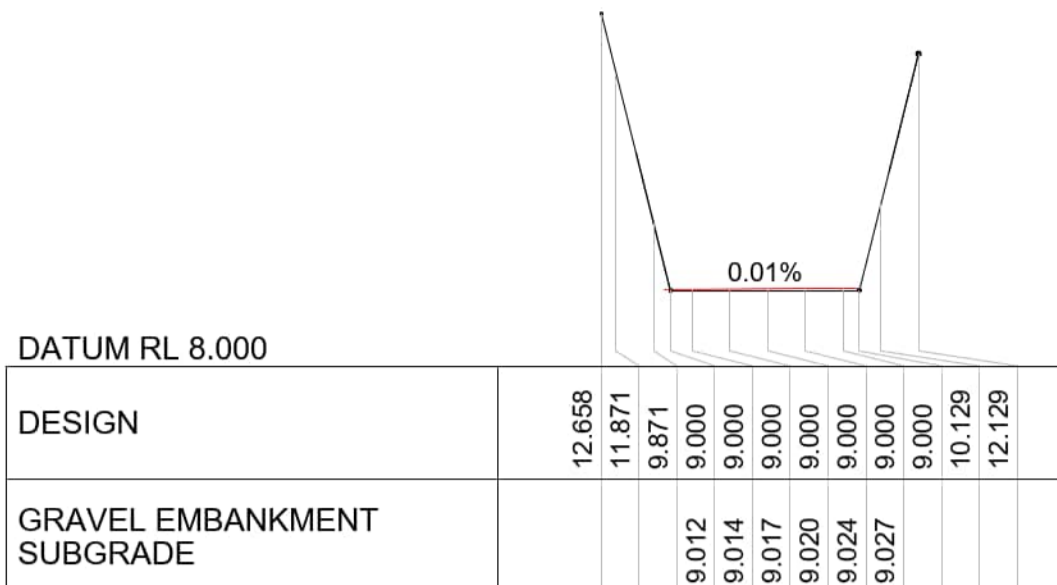


CHAINAGE 220

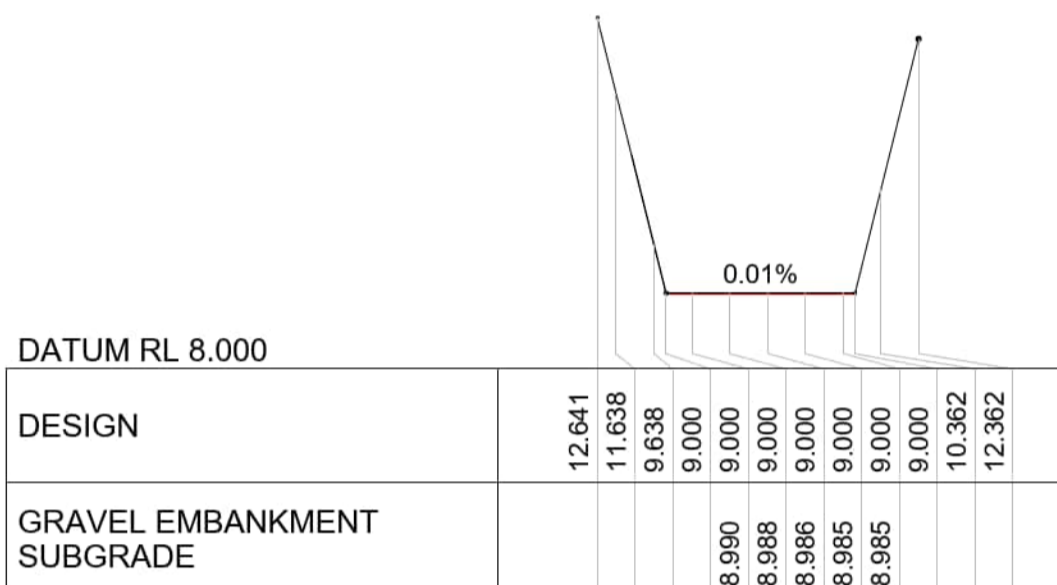


CHAINAGE 200

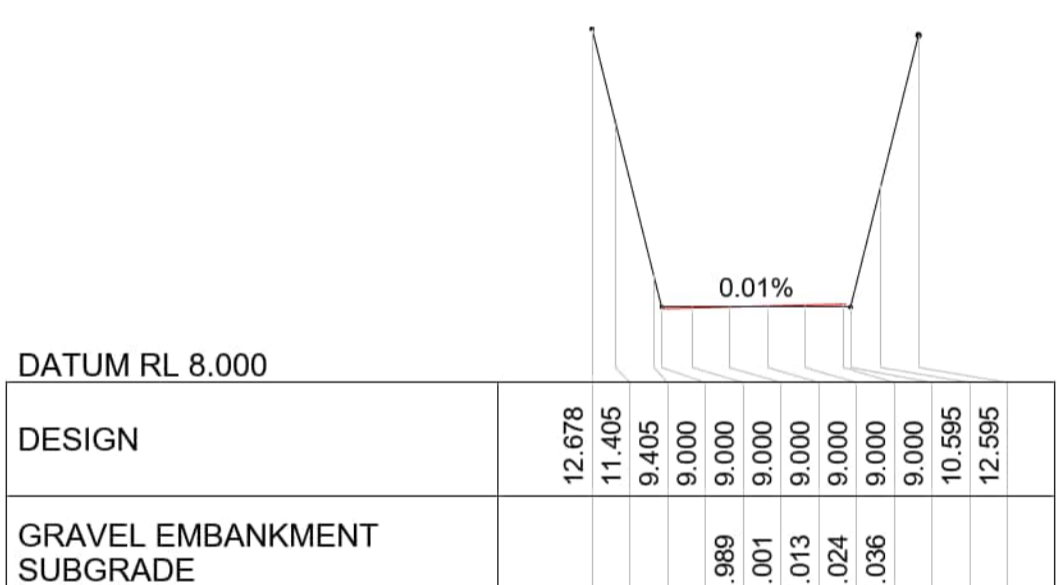


CHAINAGE 180

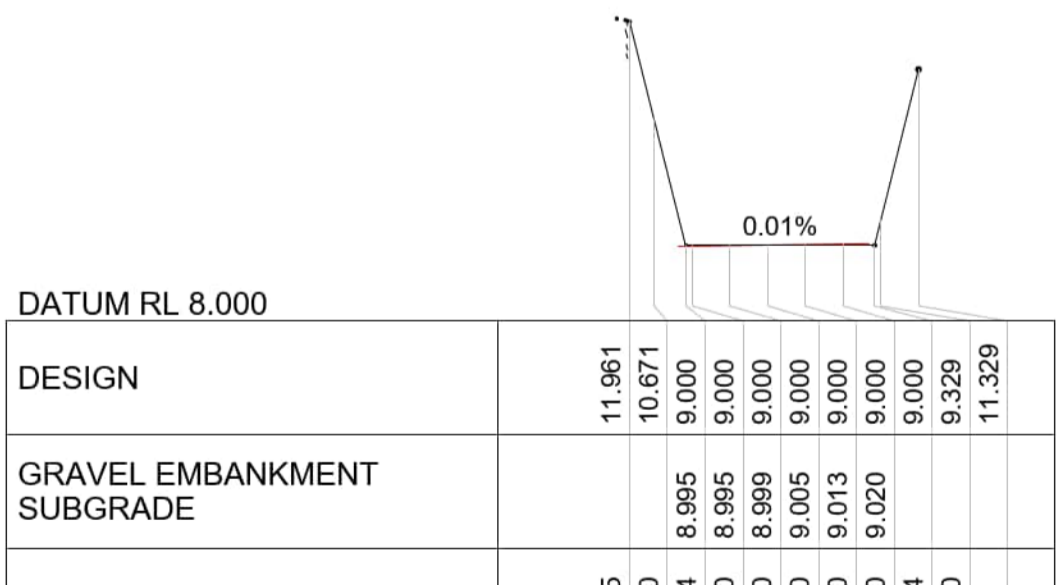


CHAINAGE 160

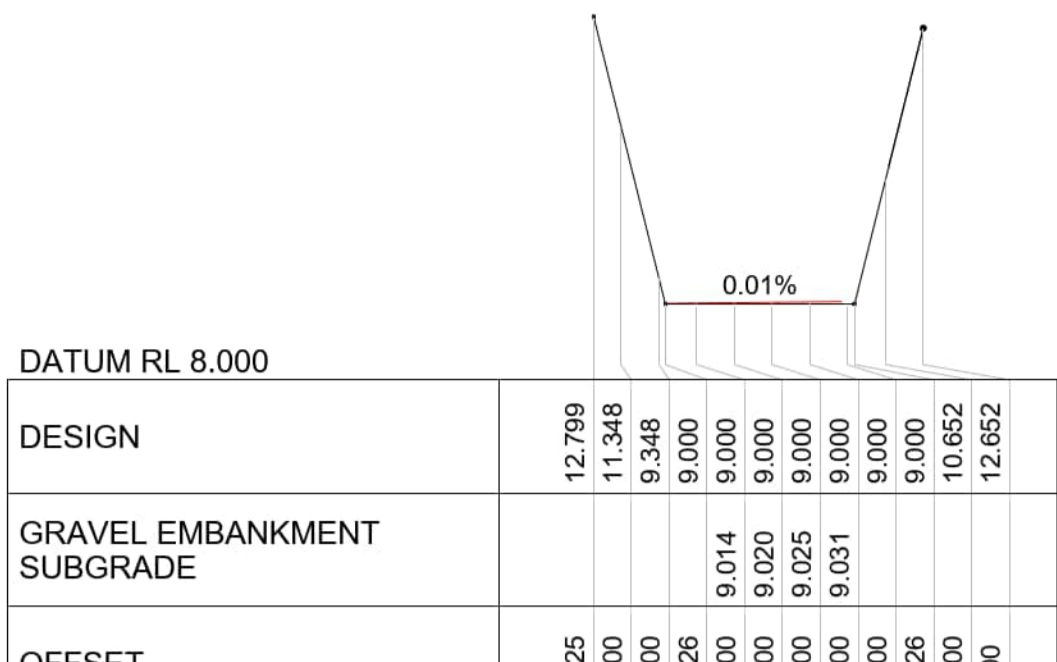


CHAINAGE 300

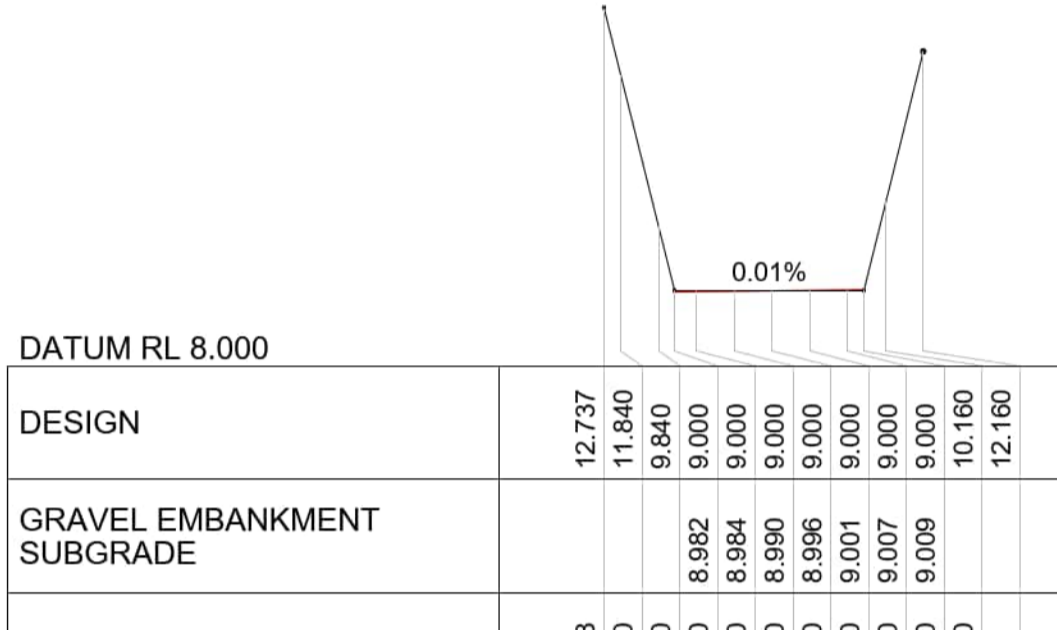


CHAINAGE 280







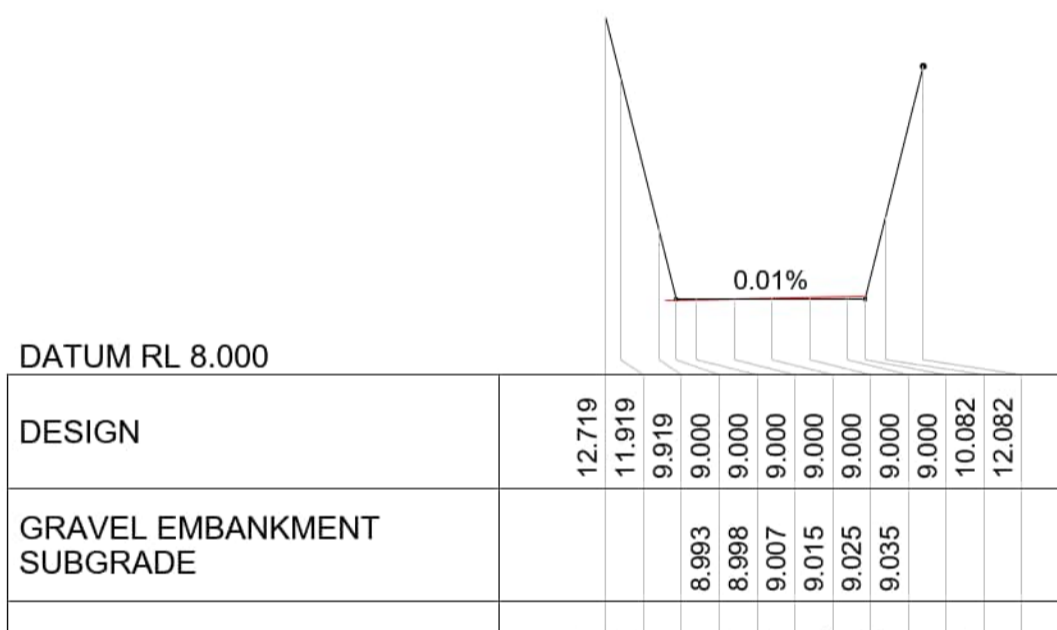


CHAINAGE 260

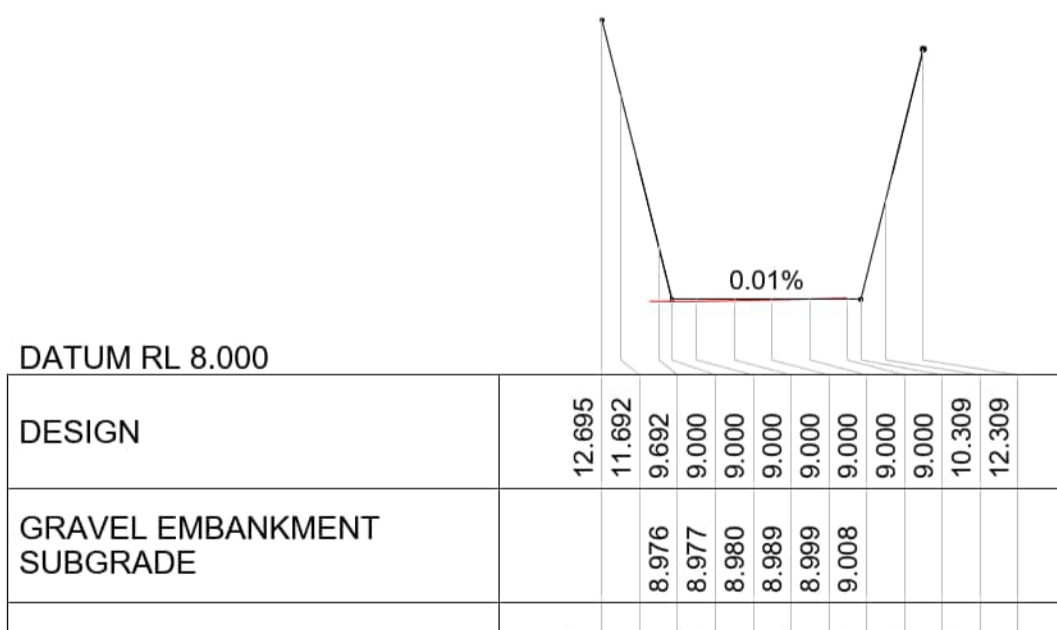

CHAINAGE 240



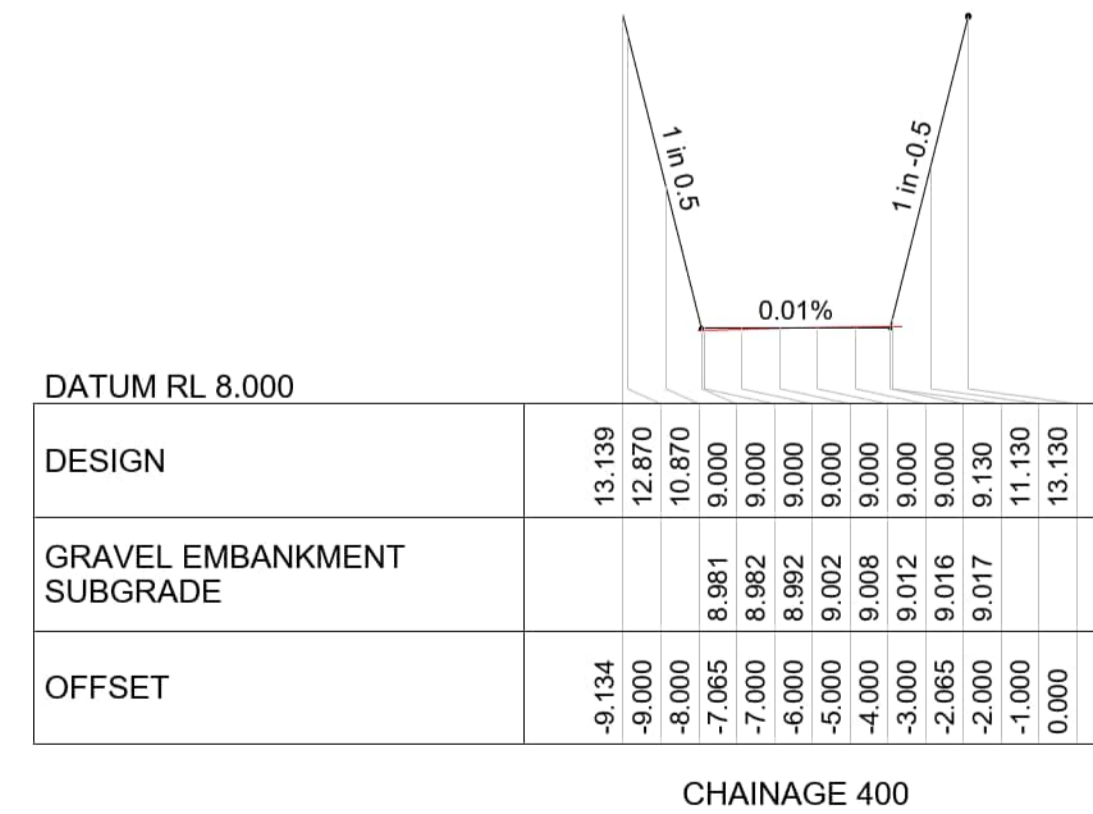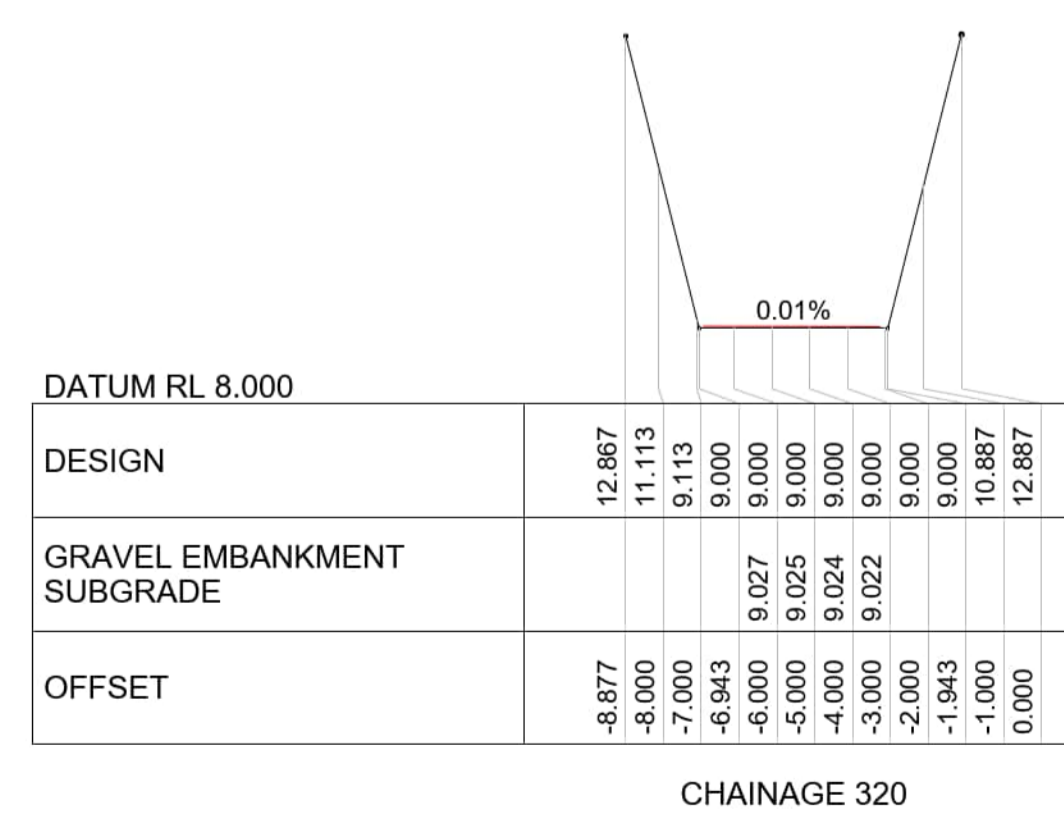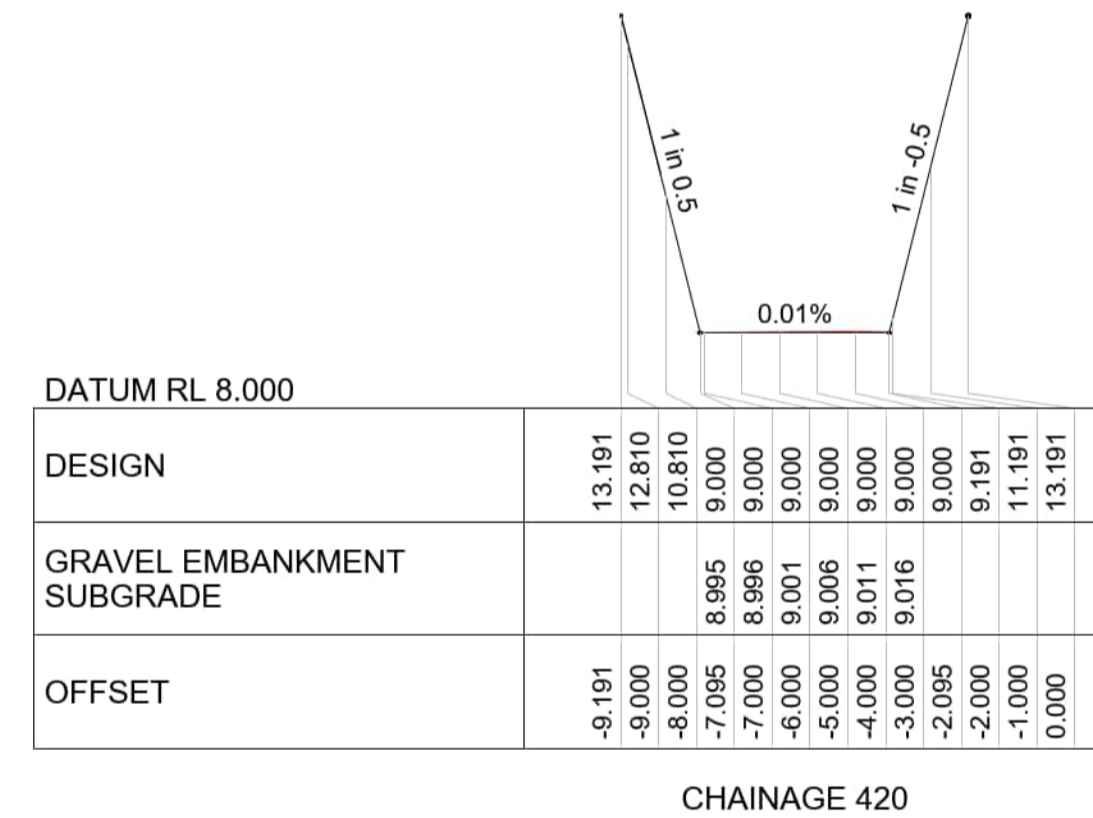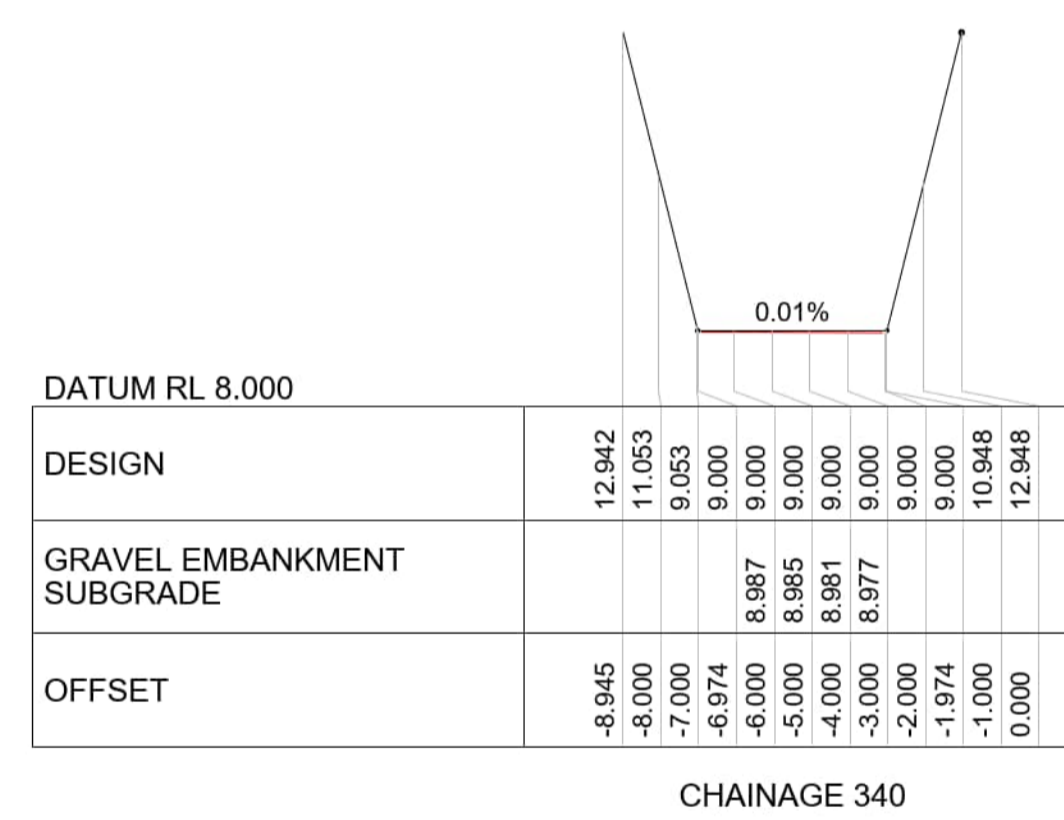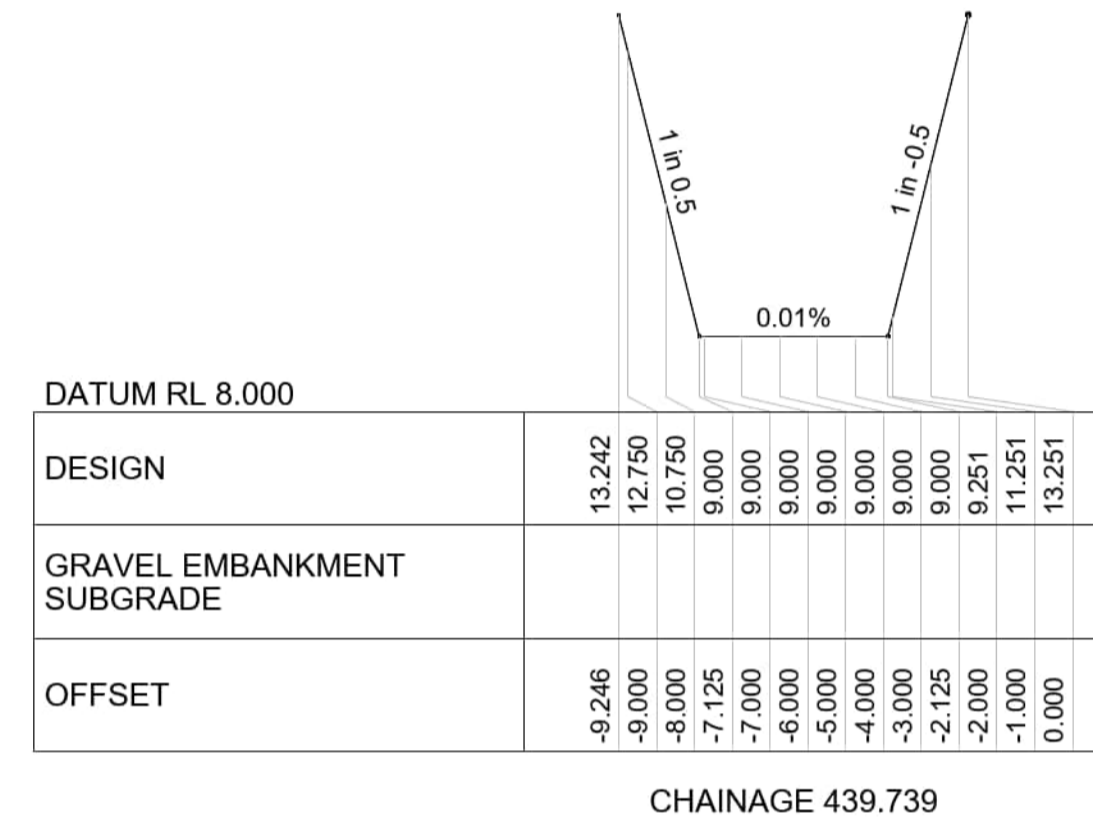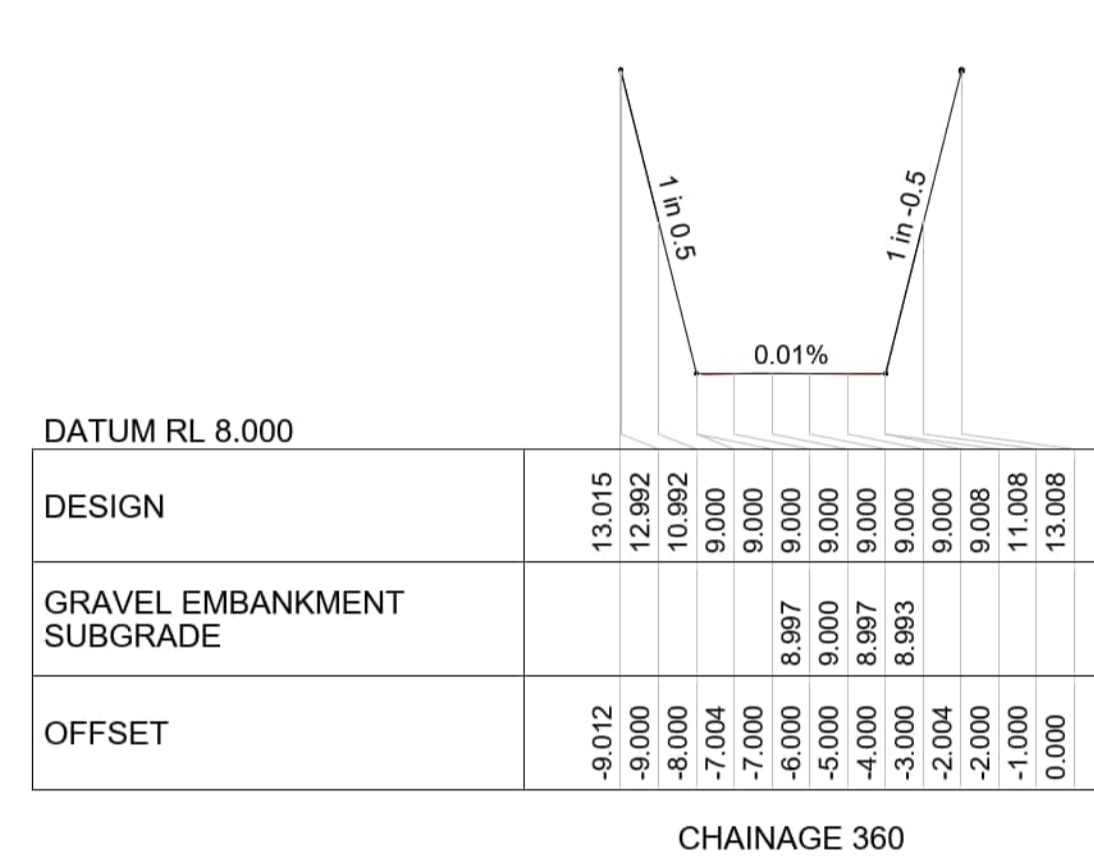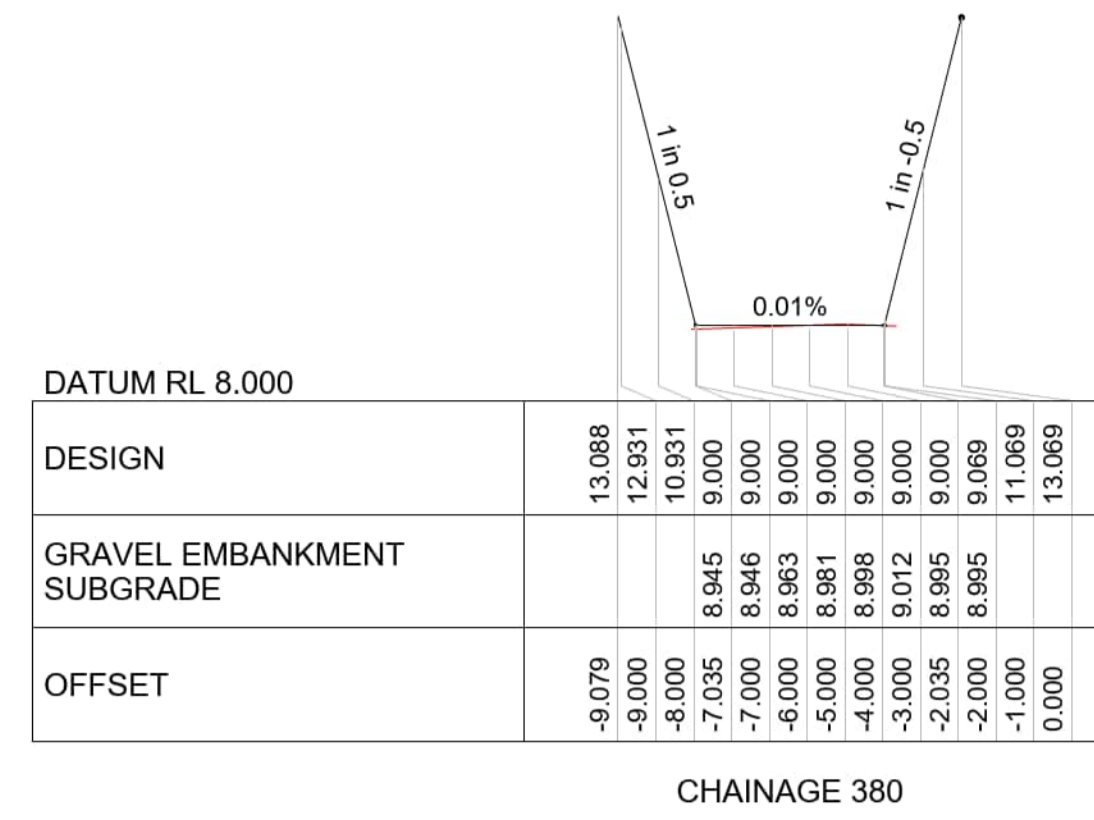

REV	DATE	REVISION DETAILS	APPROVED	DRAWN A. COLUMBUS	DESIGNED M. CROWE	PROJECT		TENDER	
						PRESTONS PARK		PROJECT No. 235361	
				CHECKED				SCALE 1:200(m)	SIZE A1
				APPROVED		TITLE		DRAWING No.	REV
					DATE	STAGE 5 GRAVEL EMBANKMENT AS BUILT CROSS SECTION SHEET 2 OF 2		LD-PS-S5-EW-14	A
A	20/10/22	AS BUILT ISSUE							



Appendix E

Post Earthworks CPT Testing

CONE PENETRATION TEST (CPT) REPORT



Client: Aurecon NZ Ltd

Location: Prestons Park, Christchurch


Printed: 09/05/2022

Client:	Aurecon NZ Ltd	Bore No.:	CPTu301
Project:	Prestons Park, Christchurch	Job No.:	20882

Date: 6/5/2022

Rig Operator: B. Wilson

Equipment: Geomil Panther 100

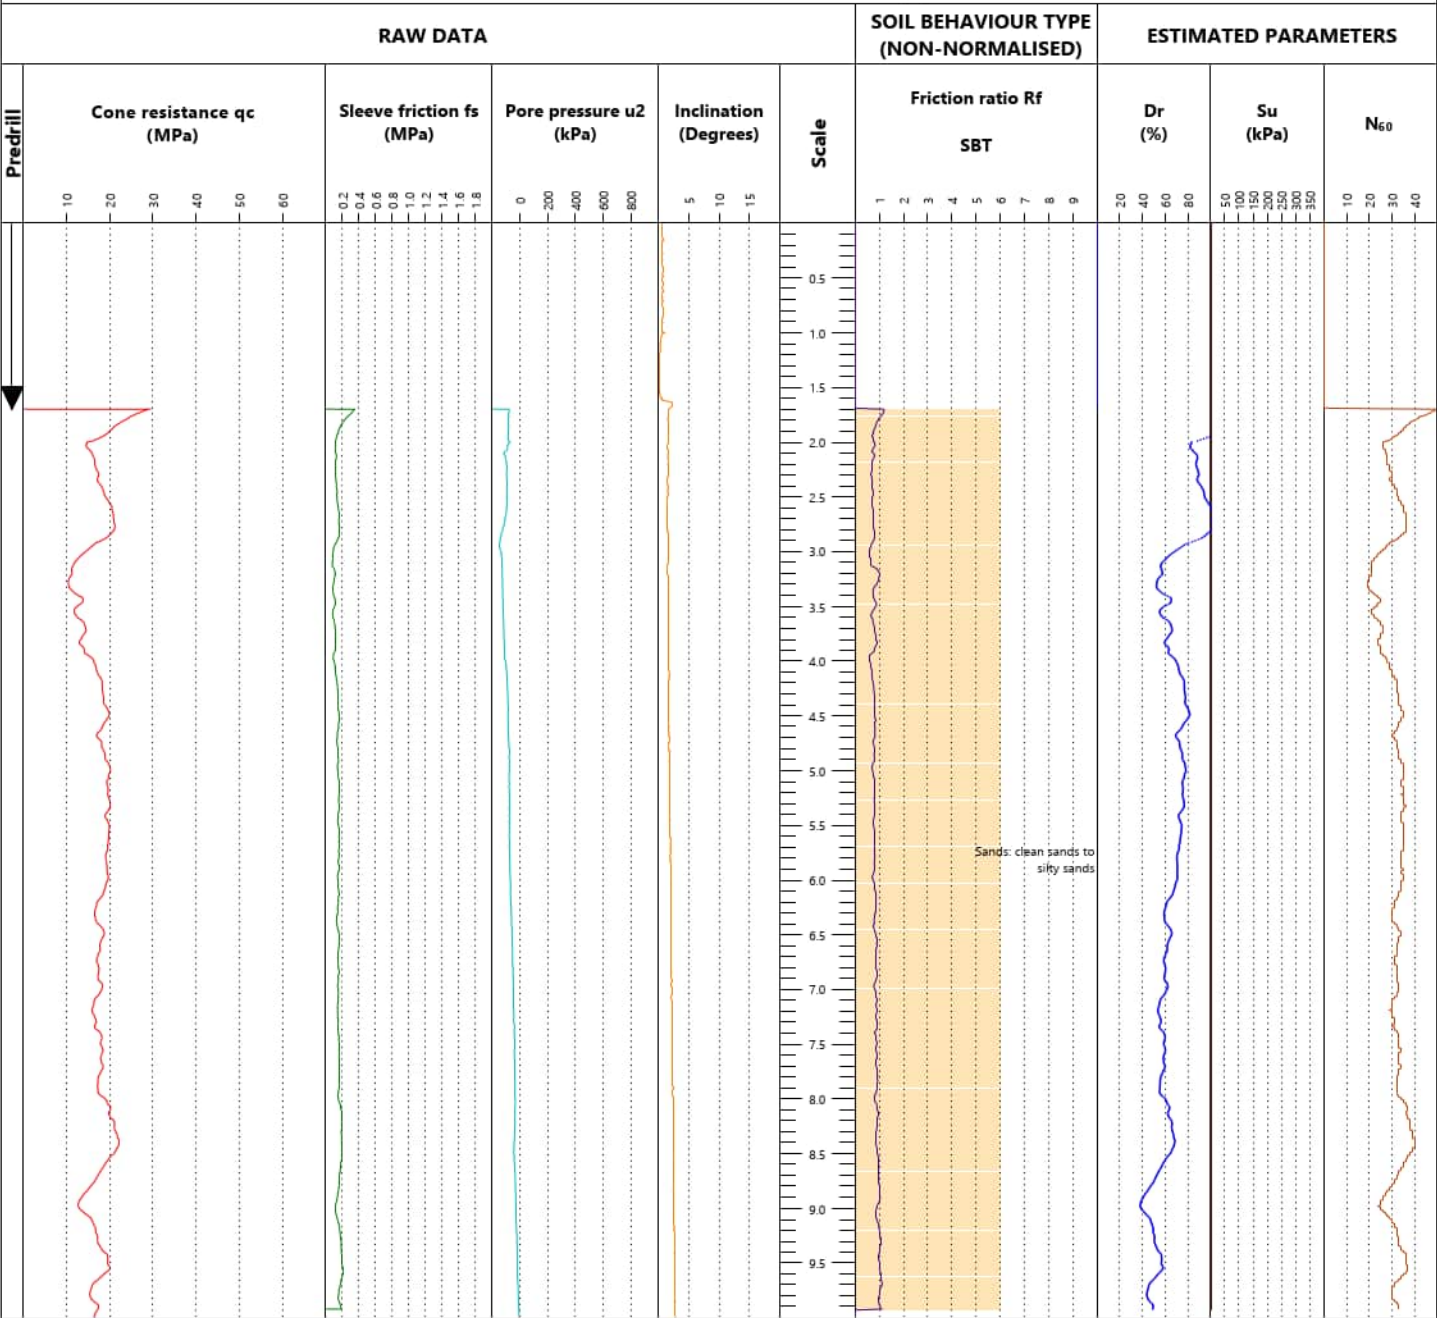

EOH: 10m

Cone Type: I-CFXYP20-10 - Compression
Cone Reference: 100992
Cone Area Ratio: 0.75
Standards: ISO 22476-1:2012

Predrill: 1.70m
Water Level: -
Collapse: 2.2m

Termination

Target Depth ☒

Effective Refusal

Tip	
Gauge	
Inclinometer	
Other	

Soil Behaviour Type (SBT) - Robertson et al. 1986

0	Undefined	5	Sand mixtures: silty sand to sandy silt
1	Sensitive fine-grained	6	Sands: clean sands to silty sands
2	Clay - organic soil	7	Dense sand to gravelly sand
3	Clays: clay to silty clay	8	Stiff sand to clayey sand
4	Silt mixtures: clayey silt & silty clay	9	Stiff fine-grained

Zero load outputs (MPa)	Before test	After test
Tip Resistance	0.9252	0.8986
Local Friction	0.0266	0.0265
Pore Pressure	0.0146	0.0130


Notes & Limitations

Data shown on this report has been assessed to provide a basic interpretation in terms of Soil Behaviour Type (SBT) and various geotechnical soil and design parameters using methods published in P. K. Robertson and K.L. Cabal, Guide to Cone Penetration Testing for Geotechnical Engineering. The interpretations are presented only as a guide for geotechnical use, and should be carefully reviewed by the user. No warranty is provided as to the correctness or the applicability of any of the geotechnical soil and design parameters shown and does not assume any liability for any use of the results in any design or review. The user should be fully aware of the techniques and limitations of any method used to derive data shown in this report.

Remarks

Client:	Aurecon NZ Ltd	Bore No.:	CPTu302
Project:	Prestons Park, Christchurch	Job No.:	20882

Site Location: Prestons Park, Christchurch	Date: 6/5/2022
Grid Reference: 1573767m E, 5185686.4m N (NZTM) - Map or aerial photograph	Rig Operator: B. Wilson
Elevation: 0.00m	Equipment: Geomil Panther 100
Datum: Ground	

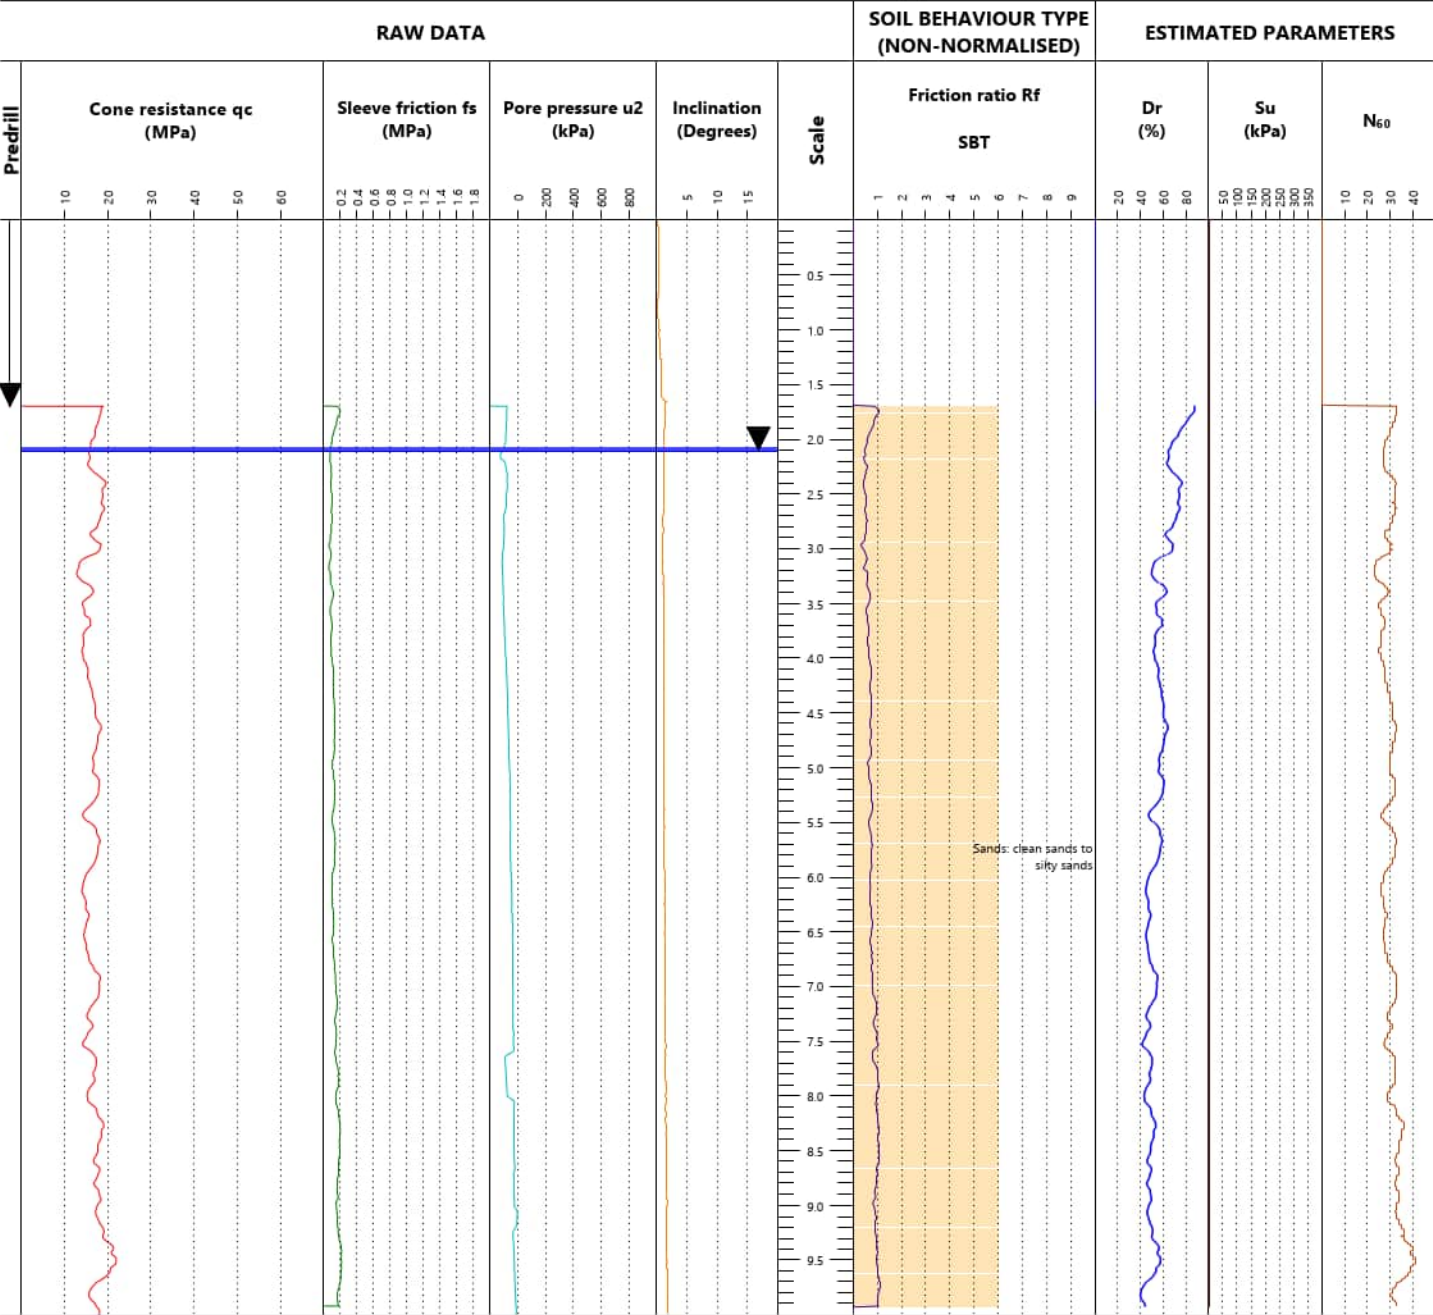

EOH: 10m

Cone Type: I-CFYP20-10 - Compression	Predrill: 1.70m	Termination	Soil Behaviour Type (SBT) - Robertson et al. 1986
Cone Reference: 100992	Water Level: 2.10m	Target Depth <input checked="" type="checkbox"/>	0 Undefined
Cone Area Ratio: 0.75	Collapse: 2.2m	Effective Refusal	1 Sensitive fine-grained
Standards: ISO 22476-1:2012		Tip <input type="checkbox"/>	2 Clay - organic soil
Zero load outputs (MPa)	Before test	Gauge <input type="checkbox"/>	3 Clays: clay to silty clay
Tip Resistance	0.9258	Inclinometer <input type="checkbox"/>	4 Silt mixtures: clayey silt & silty clay
Local Friction	0.0286	Other <input type="checkbox"/>	5 Sand mixtures: silty sand to sandy silt
Pore Pressure	0.0180		6 Sands: clean sands to silty sands
	0.0157		7 Dense sand to gravelly sand
			8 Stiff sand to clayey sand
			9 Stiff fine-grained


Notes & Limitations	Remarks
Data shown on this report has been assessed to provide a basic interpretation in terms of Soil Behaviour Type (SBT) and various geotechnical soil and design parameters using methods published in P. K. Robertson and K.L. Cabal, Guide to Cone Penetration Testing for Geotechnical Engineering. The interpretations are presented only as a guide for geotechnical use, and should be carefully reviewed by the user. No warranty is provided as to the correctness or the applicability of any of the geotechnical soil and design parameters shown and does not assume any liability for any use of the results in any design or review. The user should be fully aware of the techniques and limitations of any method used to derive data shown in this report.	
	Sheet 1 of 1

Client:	Aurecon NZ Ltd	Bore No.:	CPTu303
Project:	Prestons Park, Christchurch	Job No.:	20882

Date: 6/5/2022

Rig Operator: B. Wilson

Equipment: Geomil Panther 100

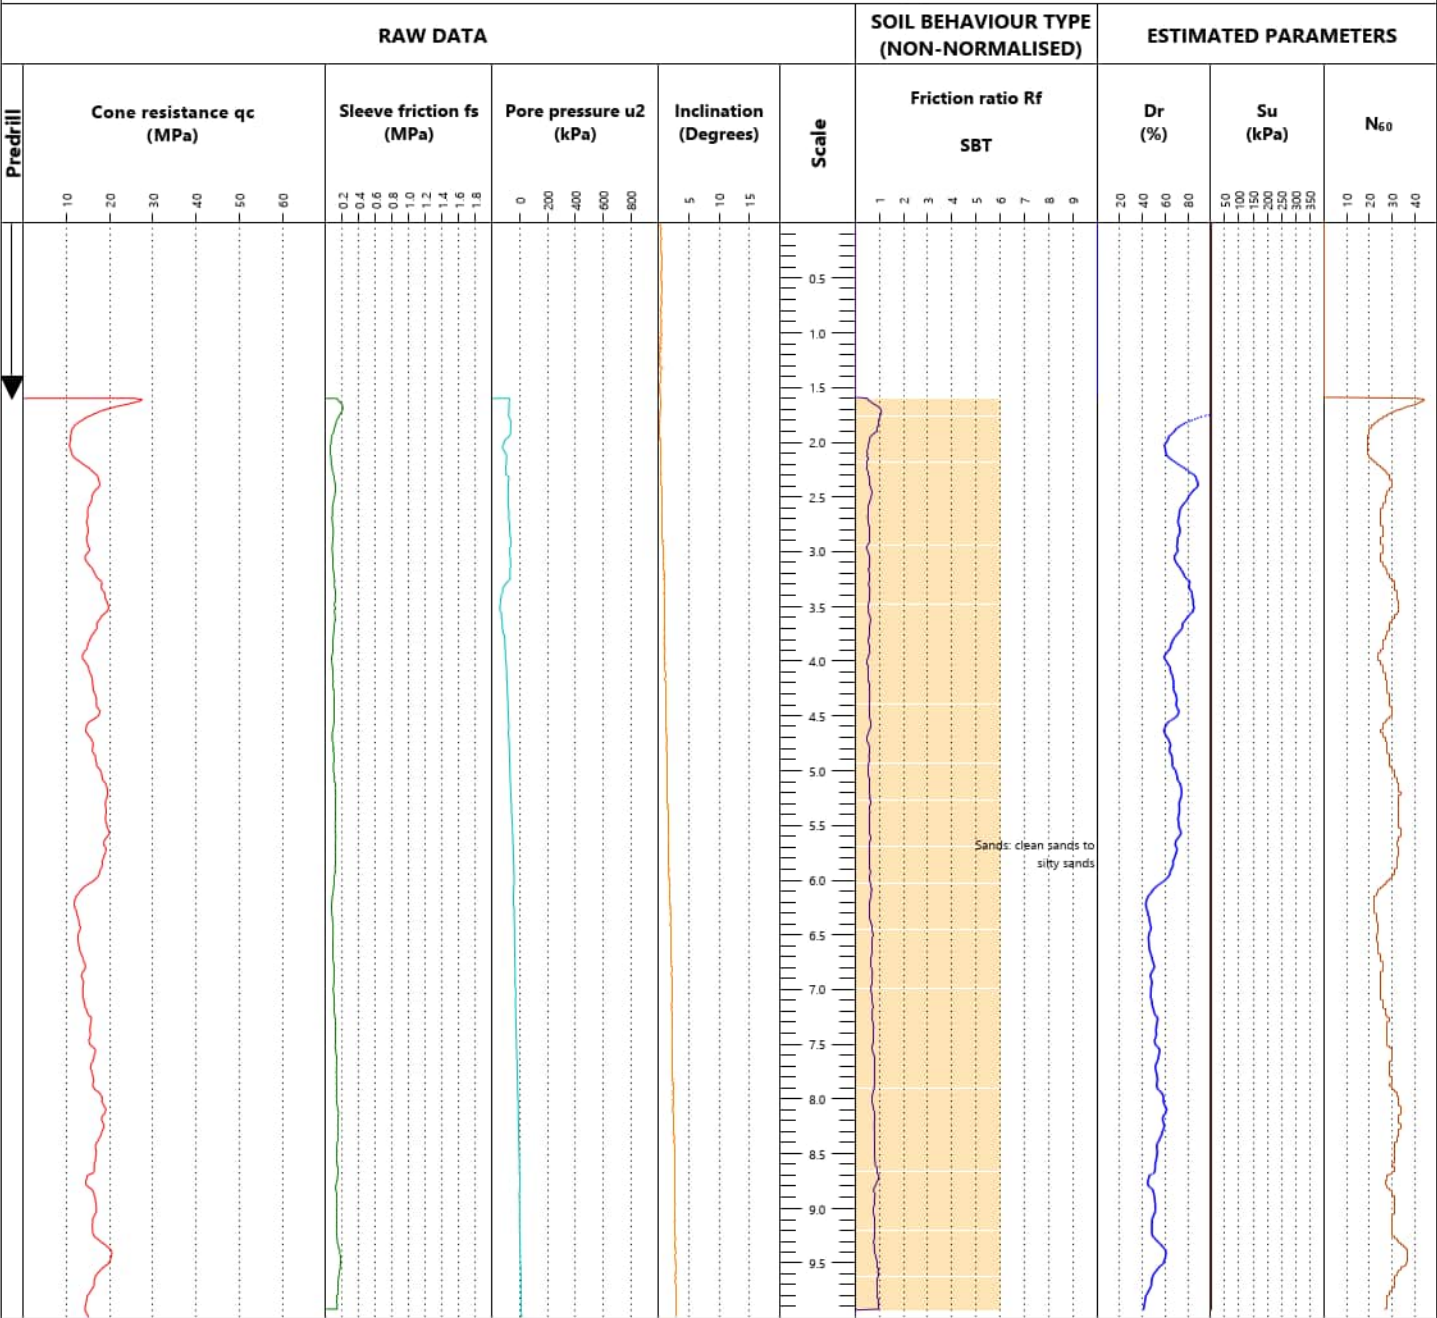

EOH: 10m

Cone Type: I-CFXYP20-10 - Compression
Cone Reference: 111007
Cone Area Ratio: 0.75
Standards: ISO 22476-1:2012

Predrill: 1.60m
Water Level: -
Collapse: 2.05m

Termination

Target Depth ☒

Effective Refusal

Tip	
Gauge	
Inclinometer	
Other	

Soil Behaviour Type (SBT) - Robertson et al. 1986

0	Undefined	5	Sand mixtures: silty sand to sandy silt
1	Sensitive fine-grained	6	Sands: clean sands to silty sands
2	Clay - organic soil	7	Dense sand to gravelly sand
3	Clays: clay to silty clay	8	Stiff sand to clayey sand
4	Silt mixtures: clayey silt & silty clay	9	Stiff fine-grained

Zero load outputs (MPa)	Before test	After test
Tip Resistance	0.1578	0.1308
Local Friction	0.0047	0.0049
Pore Pressure	-0.0074	-0.0116

Notes & Limitations

Data shown on this report has been assessed to provide a basic interpretation in terms of Soil Behaviour Type (SBT) and various geotechnical soil and design parameters using methods published in P. K. Robertson and K.L. Cabal, Guide to Cone Penetration Testing for Geotechnical Engineering. The interpretations are presented only as a guide for geotechnical use, and should be carefully reviewed by the user. No warranty is provided as to the correctness or the applicability of any of the geotechnical soil and design parameters shown and does not assume any liability for any use of the results in any design or review. The user should be fully aware of the techniques and limitations of any method used to derive data shown in this report.

Remarks

TEST DETAIL

PointID: CPTu301
Sounding: 1

Operator: B. Wilson
Cone Type: I-CFYYP20-10 - Compression
Cone Reference: 100992
Cone Area Ratio: 0.75

Zero load outputs (MPa)	Before test	After test
Tip Resistance	0.9252	0.8986
Local Friction	0.0266	0.0265
Pore Pressure	0.0146	0.0130

Date: 6/5/2022
Predrill: 1.70m
Water Level: -
Collapse: 2.2m

Termination

Target Depth ☒

Effective Refusal

Tip ☐
Gauge ☐
Inclinometer ☐
Other ☐

PointID: CPTu302
Sounding: 2

Operator: B. Wilson
Cone Type: I-CFYYP20-10 - Compression
Cone Reference: 100992
Cone Area Ratio: 0.75

Zero load outputs (MPa)	Before test	After test
Tip Resistance	0.9258	0.9206
Local Friction	0.0286	0.0272
Pore Pressure	0.0180	0.0157

Date: 6/5/2022
Predrill: 1.70m
Water Level: 2.10m
Collapse: 2.2m

Termination

Target Depth ☒

Effective Refusal

Tip ☐
Gauge ☐
Inclinometer ☐
Other ☐

PointID: CPTu303
Sounding: 3

Operator: B. Wilson
Cone Type: I-CFYYP20-10 - Compression
Cone Reference: 111007
Cone Area Ratio: 0.75

Zero load outputs (MPa)	Before test	After test
Tip Resistance	0.1578	0.1308
Local Friction	0.0047	0.0049
Pore Pressure	-0.0074	-0.0116

Date: 6/5/2022
Predrill: 1.60m
Water Level: -
Collapse: 2.05m

Termination

Target Depth ☒

Effective Refusal

Tip ☐
Gauge ☐
Inclinometer ☐
Other ☐



CPT CALIBRATION AND TECHNICAL NOTES

These notes describe the technical specifications and associated calibration references pertaining to the following cone types:

- I-CFXY-10 measuring cone resistance, sleeve friction and inclination (standard cone, 10cm²);
- I-CFXY-15 measuring cone resistance, sleeve friction and inclination (standard cone, 15cm²);
- I-CFXYP20-10 measuring cone resistance, sleeve friction, inclination and pore pressure (piezocone, 10cm²);
- I-CFXYP100-10 measuring cone resistance, sleeve friction, inclination and high range pore pressure (piezocone, 10cm²);
- I-C2xCFXP100-10 measuring cone resistance, high range sleeve friction, inclination and high range pore pressure (piezocone, 10cm²);
- I-C5F0p15XYP20-10 measuring sensitive cone resistance, sleeve friction, inclination and pore pressure (piezocone, 10cm²);
- I-CFXYP20-15 measuring cone resistance, sleeve friction, inclination and pore pressure (piezocone, 15cm²);

Dimensions


Dimensional specifications for all cone types are detailed below. All tolerances are routinely checked prior to testing and measurements taken are electronically recorded. All records are kept on file and available on request.

A.P. van den Berg Machinefabriek tel.: +31 (0)513-631355 info@apvandenbergh.com		DEVIATION of Straightness + MINIMUM Dimensions tip, friction jacket, cone adapter		Standards: EN ISO 22476-1 APB-standard	
Type of cone:	Icone 10 cm ²			Icone 15 cm ²	
<u>ALLOWABLE SIZE VARIATION</u>					
Diameter of tip:	$35,3 \leq d_1 \leq 36,0$			$43,2 \leq d_1 \leq 44,1$	
Diameter of centering ring CFP	$35,3 \leq d_1 \leq 36,0$			$43,2 \leq d_1 \leq 44,1$	
Diameter of friction jacket:	$d_1 \leq d_2 < d_1 + 0,35$			$d_1 \leq d_2 < d_1 + 0,43$	
Height dimension of tip edge:	$7 \leq h_e \leq 10$			$9 \leq h_e \leq 12$	
<u>PRODUCTION DIMENSIONS</u>					
Tip:	$d_1 = 35,7^{+0,2}_0$			$d_1 = 43,8^{+0,2}_0$	
Jacket (C-cone):	$d_2 = 35,7^{+0,2}_0$			$d_2 = 43,7^{+0,2}_0$	
Friction jacket (CF-cone):	$d_2 = 35,9^{+0,1}_0$			$d_2 = 44,0^{+0,1}_0$	
Tip for used cone:	$d_1 = 35,5^{+0,1}_0$			$d_1 = 43,5^{+0,1}_0$	
<u>MINIMUM DIMENSIONS</u>					
Minimum diameter jacket (C-cone):	$d_2 = 35,2$ (APB standard)			$d_2 = 43,0$ (APB standard)	
Minimum diameter friction jacket (CF-cone):	$d_2 = 35,3$			$d_2 = 43,2$	
Use "used cone"-tip when friction jacket diameter:	$d_2 \leq 35,65$			$d_2 \leq 43,7$	
Minimum diameter of cone adaptor:	$d = 35,3$			$d = 43,8$	
Maximum deviation of straightness:	1 mm on a length of 1000 mm (max. oscillation 1,0 mm.)			1 mm on a length of 1000 mm (max. oscillation: 2.0 mm)	

Tip and Local Friction sensor displacement

The different distances of the sensors are compensated depending on the cone types:


- 10cm² cones: 80mm
- 15cm² cones: 100mm



Cone area ratio

$$\alpha = B / A = 0.75$$

$$\beta = 1 - B / A = 0.25$$



CPT CALIBRATION AND TECHNICAL NOTES

Calibration

Each cone has a unique identification number that is electronically recorded and reported for each CPT test. The identification number enables the operator to compare 'zero-load offsets' to manufacturer calibrated zero-load offsets.

The recommended maximum zero-load offset for each sensor is determined as $\pm 5\%$ of the nominal measuring range.

In addition to maximum zero-load offsets, the difference in zero load offset before and after the test is limited as $\pm 2\%$ of the maximum measuring range. See table below:

	Tip (MPa)		Friction (MPa)			Pore Pressure (MPa)	
Maximum Measuring Range:	150	15 *	1.50	0.3 *	3 **	3	15 ***
Nominal Measuring Range:	75	7.5 *	1.00	0.15 *	1 **	2	10 ***
Max. 'zero-load offset':	7.5	0.75 *	0.10	0.015 *	0.1 **	0.2	1 ***
Max 'before and after test':	3	0.3 *	0.03	0.006 *	0.06 **	0.06	0.3 ***

* I-C5F0p15XYP20-10 ("sensitive")
** I-C2xFXYP100-10 (high range friction and pore water pressure sensors)
*** I-CFXYP100-10 (high range pore water pressure sensor)

Note: The zero offsets are electronically recorded and reported for each test in the same units as that of each sensor.

Calibration Certificate



a.p. van den berg

1.1 General

Probe number: 100992
 Probe type: I-CFYYP20-10
 Description: Tip 75 MPa Sleeve 1.00 MPa Inclinator 20° Pore 2MPa
 Part number: 0100277B
 Certificate number: 100992-2
 Manufacturer: A.P. van den Berg, Heerenveen (NL)
 Calibration lab.: A.P. van den Berg Ingenieursburo, IJzerweg 4, 8445 PK, Heerenveen (NL)
 Location of calibration: RvA accredited laboratory according to ISO/IEC 17025:2017
 Client: Heerenveen (NL)
 McMillan Drilling Ltd
 120 High Street
 SOUTHBRIDGE, CANTERBURY
 New Zealand

1.2 Calibration equipment

Reference measuring equipment:

DAQ MX238B 0177FD	March 2021 (HBM: 92591)
DAQ MX440B 0182F3	March 2021 (HBM: 92778)
Loadcell 100kN H54435	August 2020 (HBM: 86959 2020-07)
Loadcell 20kN D16200	July 2020 (HBM: 86871 2020-07)
Sensor 20 Bar 240310140	Sept 2020 (ZMK: 02-1194 2020-09)
ACS-080-SC00-HE2-PM 12/17 2321909	April 2021 (Trescal: 2103-24007)
Temperature logger: 620-2326 SN:170800101	March 2021 (AVANTOR 219001540)

1.3 Laboratory conditions:

Ambient temperature: 23.8 ± 2 °C

1.4 Measurement uncertainty

The expanded combined uncertainty (k=2) of the sensor at laboratory conditions was analysed according to ISO/IEC Guide 98-3:2008 and is based on the standard uncertainty of the measurement multiplied by a coverage factor k, such that the coverage probability corresponds to approximately 95%. The results of the measurement uncertainty analysis of the different parameters are as listed below:

Cone resistance	5,6 + 0,165%	(kPa)
Sleeve friction	0,17 + 0,105%	(kPa)
Pore Pressure 2 MPa sensor	4,16 + 0,037%	(kPa)
Inclination	0,42	(degrees)

1.5 Standard and method of calibration

EN ISO 22476-1 2012 Class 2

1.6 Results

The probe complies with the requirements of the above-mentioned standard and indicated calibration class. The calibrated sensors comply if the measured deviations over the nominal measuring range are within the accuracy limits of the standard (decision rule). The deviations and standard limits are shown in graphs in the Calibration Report.

Calibrated by: D.Bisschops
 Calibration Date: 23 November 2021
 Signature:

QA Manager: N.R.E. de Jong
 Date: 23 November 2021
 Signature:

Expiration date according to EN ISO 22476-1: 24 May 2022

1.7 Remarks

The calibration results only relate to the probe identified in this certificate. This new calibration certificate replaces all previously issued certificates for this probe. The calibration certificate documents the traceability to national and international standards, which realize the units of measurement according to the International System of Units (SI). This calibration certificate may not be reproduced other than in full and except with permission of the issuing laboratory. Calibration certificates without signature are not valid.

Calibration Certificate



a.p. van den berg

1.1 General

Probe number: 111007
 Probe type: I-CFXYP20-10
 Description: Tip 75 MPa Sleeve 1.00 MPa Inclinator 20° Pore 2MPa
 Part number: 0100277B
 Certificate number: 111007-5
 Manufacturer: A.P. van den Berg, Heerenveen (NL)
 Calibration lab.: A.P. van den Berg Ingenieursburo, IJzerweg 4, 8445 PK, Heerenveen (NL)
 Location of calibration: Heerenveen (NL)
 Client: McMillan Drilling Ltd
 120 High Street
 SOUTHBRIDGE, CANTERBURY
 New Zealand

1.2 Calibration equipment

Reference measuring equipment:

DAQ MX238B 00E80F	Aug 2021 (HBM: 96998 2021-08)
DAQ MX440B 00FCAB	Aug 2021 (HBM: 97005 2021-08)
Loadcell 100kN 201330120	August 2021 (HBM: 96532 2021-08)
Loadcell 20kN 210230193	Aug 2021 (HBM: 96418 2021-08)
Sensor 20 Bar 240310135	Sept 2020 (ZKM: 02-1193 2020-09)
ACS-080-SC00-HP2-PM 02/18 2610439	April 2021 (Trescal: 2103-24005)
Temperature logger: 620-2326 SN: 170800285	June 2021 (AVANTOR: 219003177)

1.3 Laboratory conditions:

Ambient temperature: 22.5 ± 2 °C

1.4 Measurement uncertainty

The expanded combined uncertainty ($k=2$) of the sensor at laboratory conditions was analysed according to ISO/IEC Guide 98-3:2008 and is based on the standard uncertainty of the measurement multiplied by a coverage factor k , such that the coverage probability corresponds to approximately 95%. The results of the measurement uncertainty analysis of the different parameters are as listed below:

Cone resistance	5,6 + 0,165%	(kPa)
Sleeve friction	0,17 + 0,105%	(kPa)
Pore Pressure 2 MPa sensor	4,16 + 0,037%	(kPa)
Inclination	0,42	(degrees)

1.5 Standard and method of calibration

EN ISO 22476-1 2012 Class 2

1.6 Results

The probe complies with the requirements of the above-mentioned standard and indicated calibration class. The calibrated sensors comply if the measured deviations over the nominal measuring range are within the accuracy limits of the standard (decision rule). The deviations and standard limits are shown in graphs in the Calibration Report.

Calibrated by:
 Calibration Date:
 Signature:

D. Bisschops
 22 February 2022

QA Manager:
 Date:
 Signature:

N.R.E. de Jong
 22 February 2022

Expiration date according to EN ISO 22476-1: 23 August 2022

1.7 Remarks

The calibration results only relate to the probe identified in this certificate. This new calibration certificate replaces all previously issued certificates for this probe. The calibration certificate documents the traceability to national and international standards, which realize the units of measurement according to the International System of Units (SI). This calibration certificate may not be reproduced other than in full and except with permission of the issuing laboratory. Calibration certificates without signature are not valid.

Certificate version 1.20

Certificate number: 111007-5

Page 1/6

Document prepared by

Aurecon New Zealand Limited

Level 2, Iwikau Building
93 Cambridge Terrace
Christchurch 8013
New Zealand

T +64 3 366 0821

F +64 3 379 6955

E christchurch@aurecongroup.com

W aurecongroup.com


aurecon

*Bringing ideas
to life*

Aurecon offices are located in:

Angola, Australia, Botswana, China,
Ghana, Hong Kong, Indonesia, Kenya,
Lesotho, Macau, Mozambique,
Namibia, New Zealand, Nigeria,
Philippines, Qatar, Singapore, South Africa,
Swaziland, Tanzania, Thailand, Uganda,
United Arab Emirates, Vietnam.



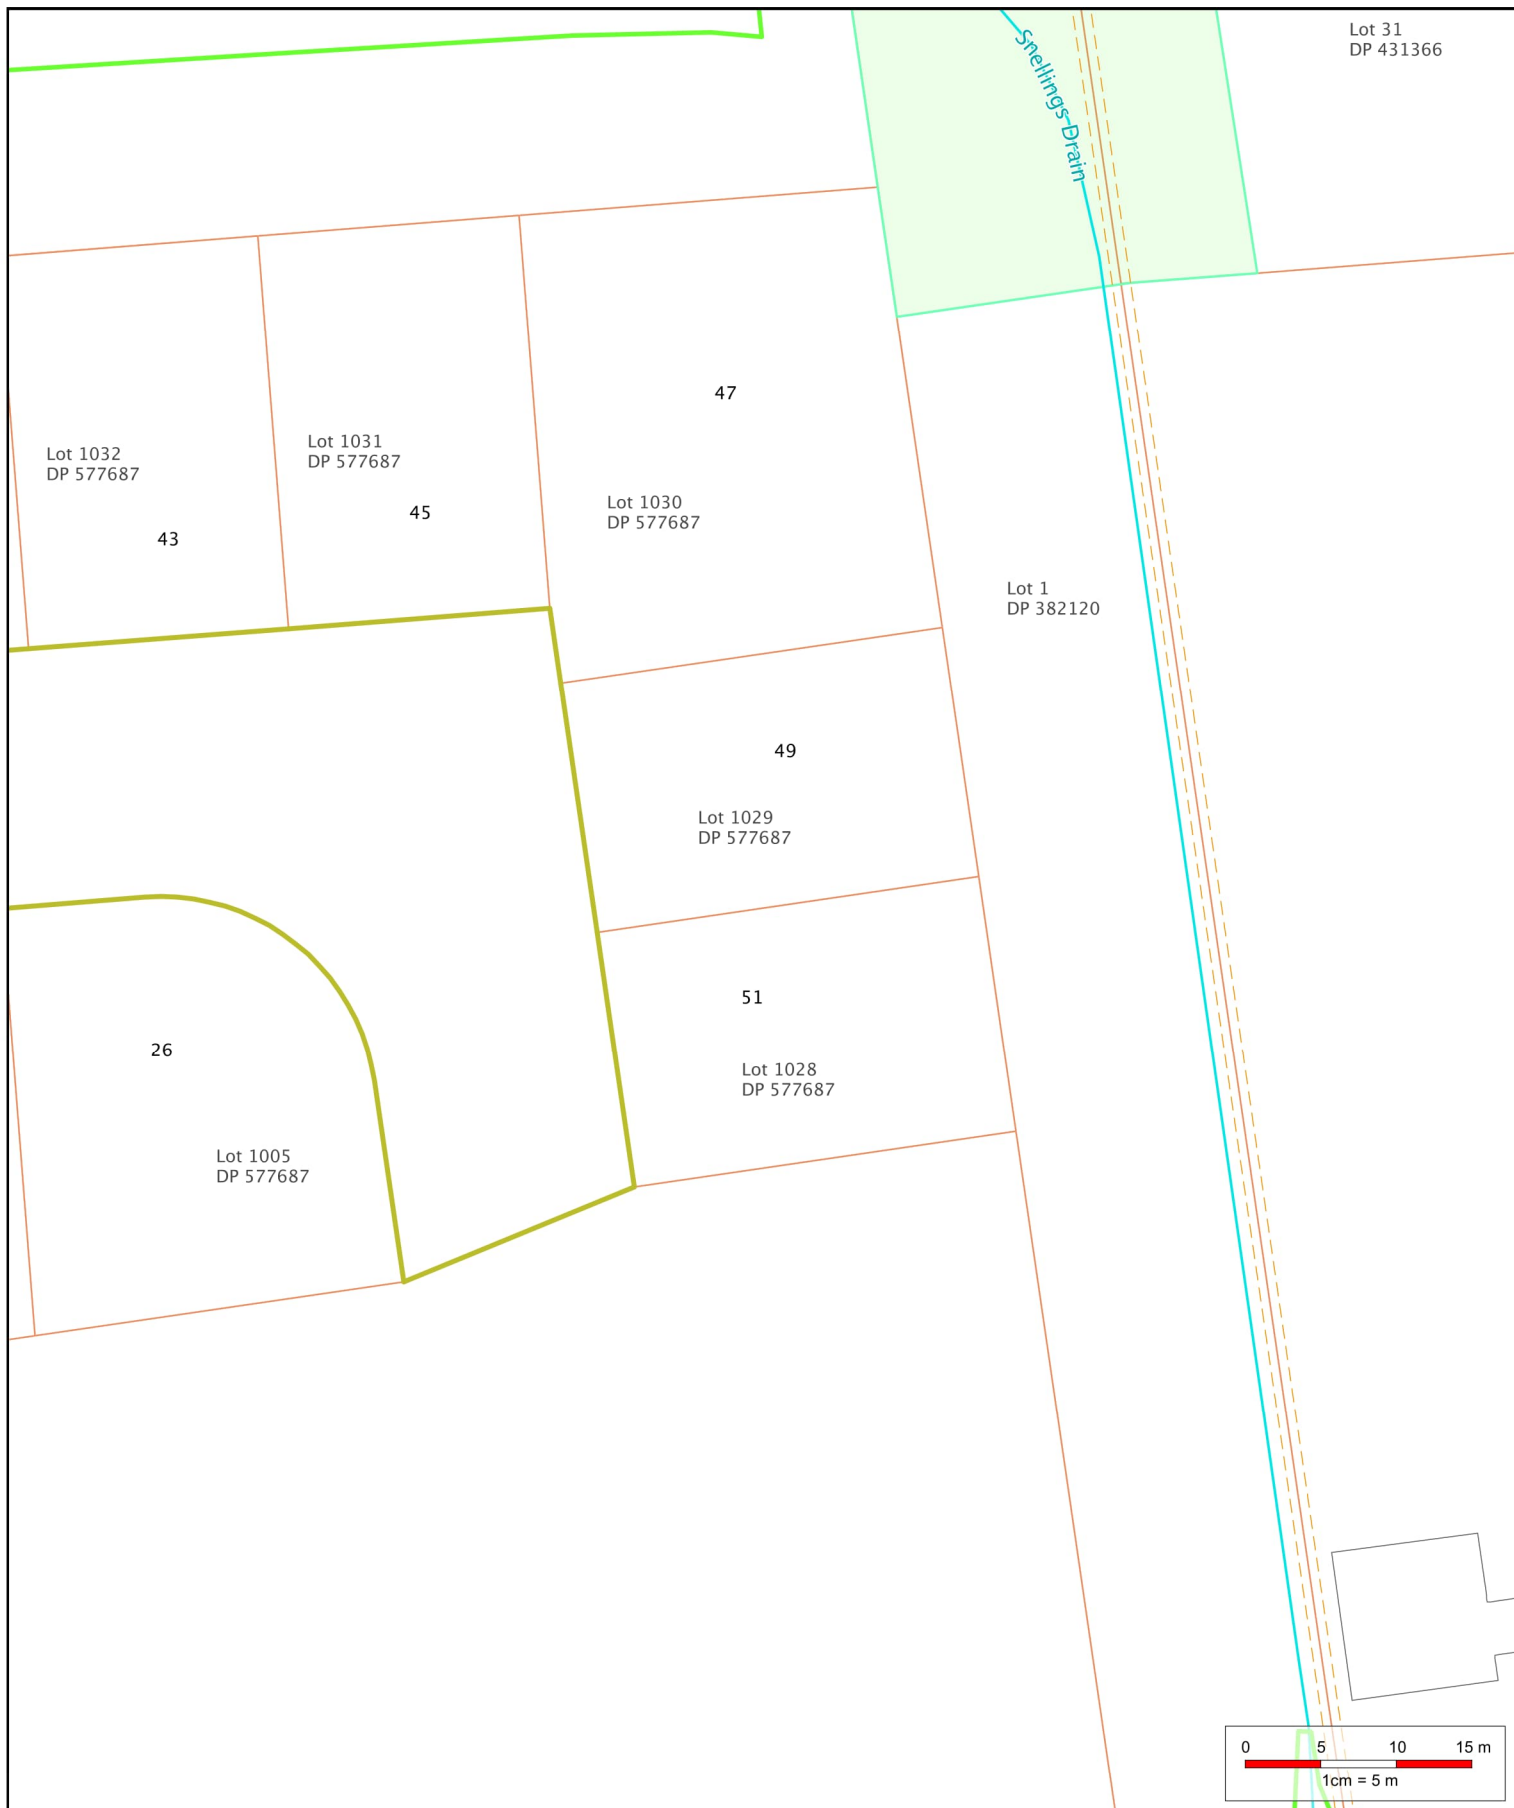

1 : 500 on A4

28/07/2023 9:00:00 AM



ph: 941-8300 fax: 941-8385

Accuracy not guaranteed. Onsite verification required. Display of data scale dependent, full detail available at 1:500.

Copyright © 2013 Reproduction prohibited

Private Drainage

Standard Infrastructure

- Bio Gas
- Condensate Trap
- End Cap
- Inlet
- Outlet
- Valve
- Main
- Cable

Water Intake/Supply

- Connector
- Bellows
- Connector
- Hydrant

Water Intake/Supply

- Inlet
- Meter
- Outlet
- Pump
- Restrictor
- Valve
- Air Release
- Butterfly
- Flow restriction
- Gate
- Pressure Activated
- Sluice
- Valve
- Reservoir
- Structure
- Lateral
- Main
- Sub Main

Wastewater

- End Cap
- Valve
- Air Gap Separator
- Vent
- Eye
- Eye (Vertical)
- Outfall
- Pump
- Junction
- Access
- Flush Manhole
- Inspection Point
- Standard Manhole
- Trap
- Vented Manhole
- Lateral
- Main
- Pressure Main

Wastewater

- Lateral Fitting
- Local Pressure
- Control Panel
- Boundary Kit
- Tank System
- Site
- Vacuum Chamber
- Vacuum Breather
- Bend
- Change
- Eye
- Flow Restriction
- Inlet
- Dome Sump
- Double Sump
- Gross Debris Trap

Stormwater

- Inlet
- Inlet Headwall
- Pipe End
- Silt Trap
- Single Sump
- Soak Pit
- Triple Sump
- Junction
- Standard Manhole
- Outlet
- Pump
- Structure
- Basin
- Lateral
- Main
- Lateral Fitting
- Double Sump

Stormwater

- Lateral Fitting
- Single Sump
- Soak Pit
- Inspection point
- Manhole
- Pipe Protection
- Abandoned
- Proposed
- Out of service
- Easement

51 Timara Crescent Land Use Consents



**51 Timara Crescent
Subdivision Consents**

Fee simple
Lots:20
Approved

Land Use Resource Consents within 100 metres of 51 Timara Crescent

Note: This list does not include subdivision Consents and Certificates of Compliance issued under the Resource Management Act.

155R Mairehau Road

RMA/2020/170

Earthworks within setback from Snellings Drain associated with the installation of new stormwater outfall pipes, culvert and removal of existing bridge

Cancelled

Applied 30/01/2020

Cancelled - fee not paid 04/03/2020

RMA/2021/1436

Earthworks within 5m setback of a network waterway associated with the naturalisation of Snellings Drain

Processing complete

Applied 19/05/2021

Decision issued 25/06/2021

Granted 25/06/2021

205 Mairehau Road

RMA/2022/1180

Subdivision - Fee simple - 20 Lots with earthworks

Consent issued

Applied 14/04/2022

Decision issued 15/02/2023

Granted 14/02/2023

25 Cameo Grove

RMA/2017/2545

To construct buildings on Lots 291-294, 312-318 and 377-389 (Stage 2) up to 4 m from the Mairehau Road boundary and with a reduced landscaping strip of 2m in width

Processing complete

Applied 17/10/2017

Decision issued 17/01/2018

Granted 17/01/2018

29 Araucana Way

RMA/2013/187

Proposed new dwelling with attached garage - Historical Reference RMA92021774

Processing complete

Applied 08/02/2013

Decision issued 04/03/2013

Granted 01/03/2013

31 Araucana Way

RMA/2018/3127

Construct dwelling with attached garage

Processing complete

Applied 20/12/2018

Decision issued 30/01/2019

Granted 30/01/2019

42 McKerrow Street

RMA/2017/2545

To construct buildings on Lots 291-294, 312-318 and 377-389 (Stage 2) up to 4 m from the Mairehau Road boundary and with a reduced landscaping strip of 2m in width

Processing complete

Applied 17/10/2017

Decision issued 17/01/2018

Granted 17/01/2018

8R Araucana Way

RMA/2021/1436

Earthworks within 5m setback of a network waterway associated with the naturalisation of Snellings Drain

Processing complete

Applied 19/05/2021

Decision issued 25/06/2021

Granted 25/06/2021

Data Quality Statement

Land Use Consents

All resource consents are shown for sites that have been labelled with an address. For sites that have been labelled with a cross (+) no resource consents have been found. Sites that have no label have not been checked for resource consents. This will be particularly noticeable on the margins of the search radius. If there are such sites and you would like them included in the check, please ask for the LIM spatial query to be rerun accordingly. This will be done free of charge although there may be a short delay. Resource consents which are on land occupied by roads, railways or rivers are not, and currently cannot be displayed, either on the map or in the list. Resource consents that relate to land that has since been subdivided, will be shown in the list, but not on the map. They will be under the address of the land as it was at the time the resource consent was applied for. Resource consents that are listed as Non-notified and are current, may in fact be notified resource consents that have not yet been through the notification process. If in doubt. Please phone (03)941 8999.

The term “resource consents” in this context means land use consents. Subdivision consents and certificates of compliance are excluded.

Subdivision Consents

All subdivision consents are shown for the sites that have been labelled with consent details. For Sites that have been labelled with a cross (+) no records have been found. Sites that have no label have not been checked for subdivision consents. This will be particularly noticeable on the margins of the search radius. If there are such sites and you would like them included in the check, please ask for the LIM spatial query to be rerun accordingly. This will be done free of charge although there may be a short delay.

The term “subdivision consents” in this context means a resource consent application to subdivide land. Non subdivision land use resource consents and certificates of compliance are excluded.

This report will only record those subdivision applications which have not been completed i.e once a subdivision has been given effect to and the new lots/properties have been established the application which created those lots will not be shown

All subdivision consent information is contained on the map and no separate list is supplied
